




Explosives in Groundwater Compared to Maximum Contaminant Level/Health Advisories Validated Data as of 08/26/05

FIGURE 1

AMEC Earth & Environmental, Inc.
Westford, Massachusetts

J:\GIS\Sept2005\Monthly\1_Exp\Exp_overall.pdf
 G:\MMR_COE\Work2005\Monthly\Sept2005\1_Exp\Exp_overall.mxd
 September 1, 2005 DWN: DNB JBB ABF CHKD: MD

Impact Area Groundwater Study Program

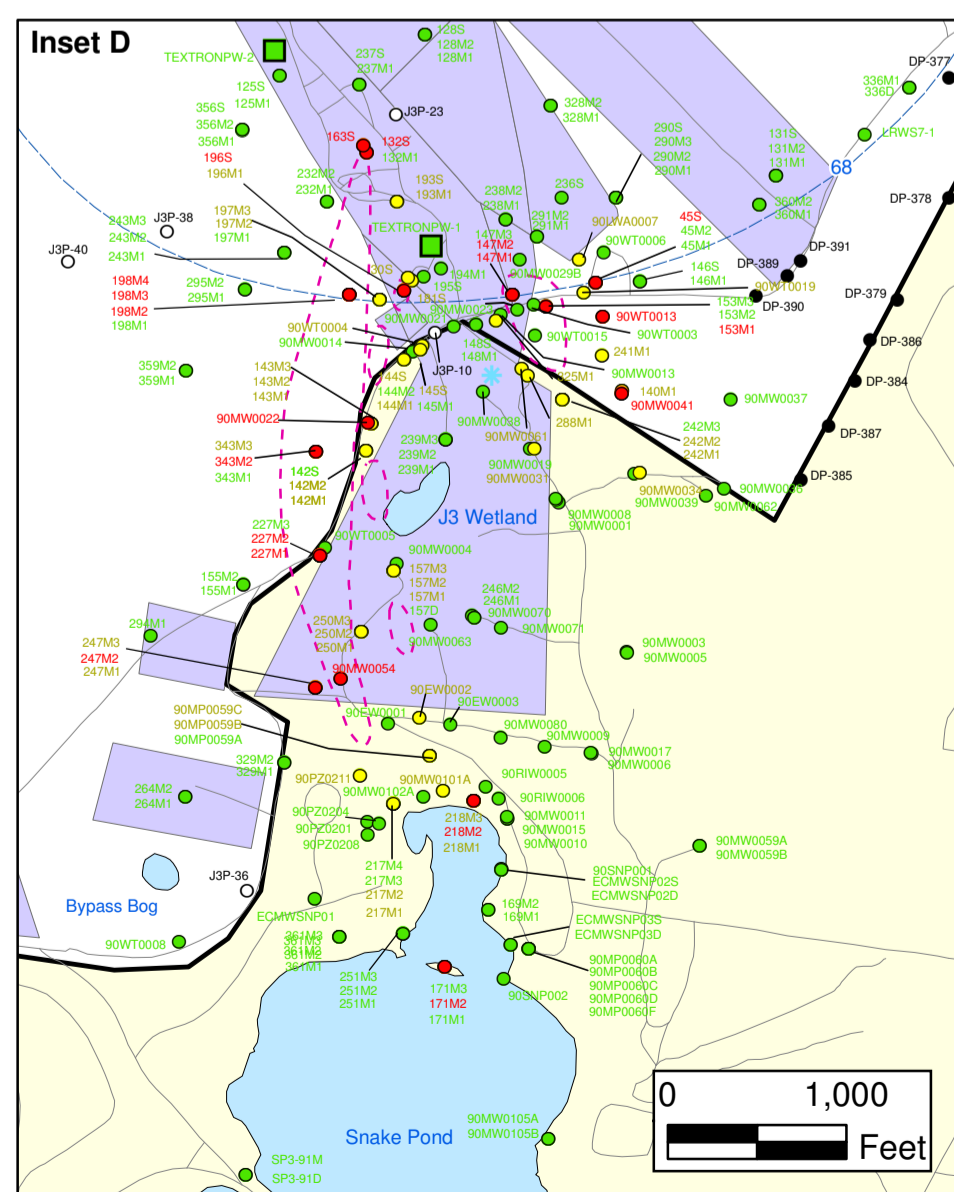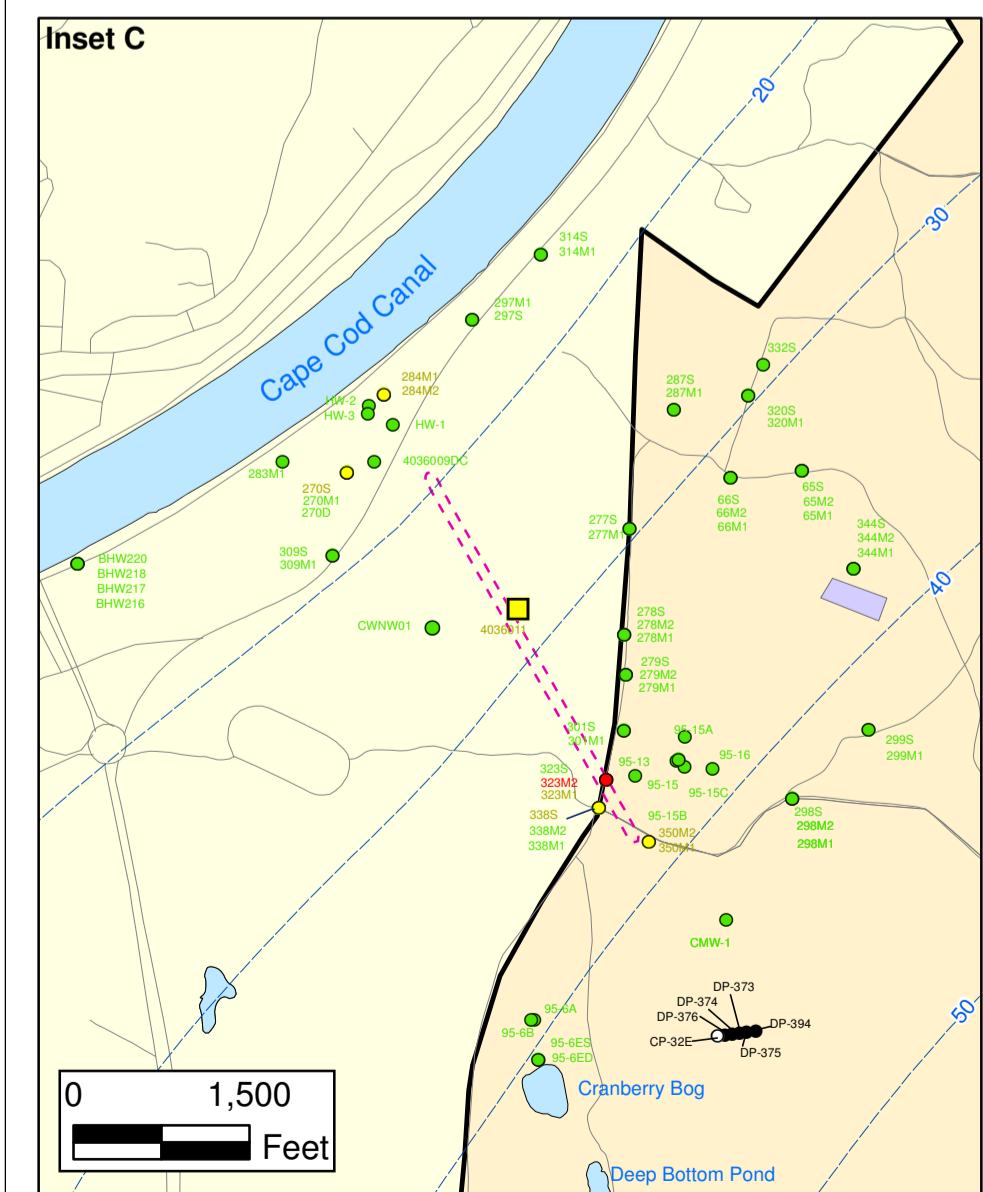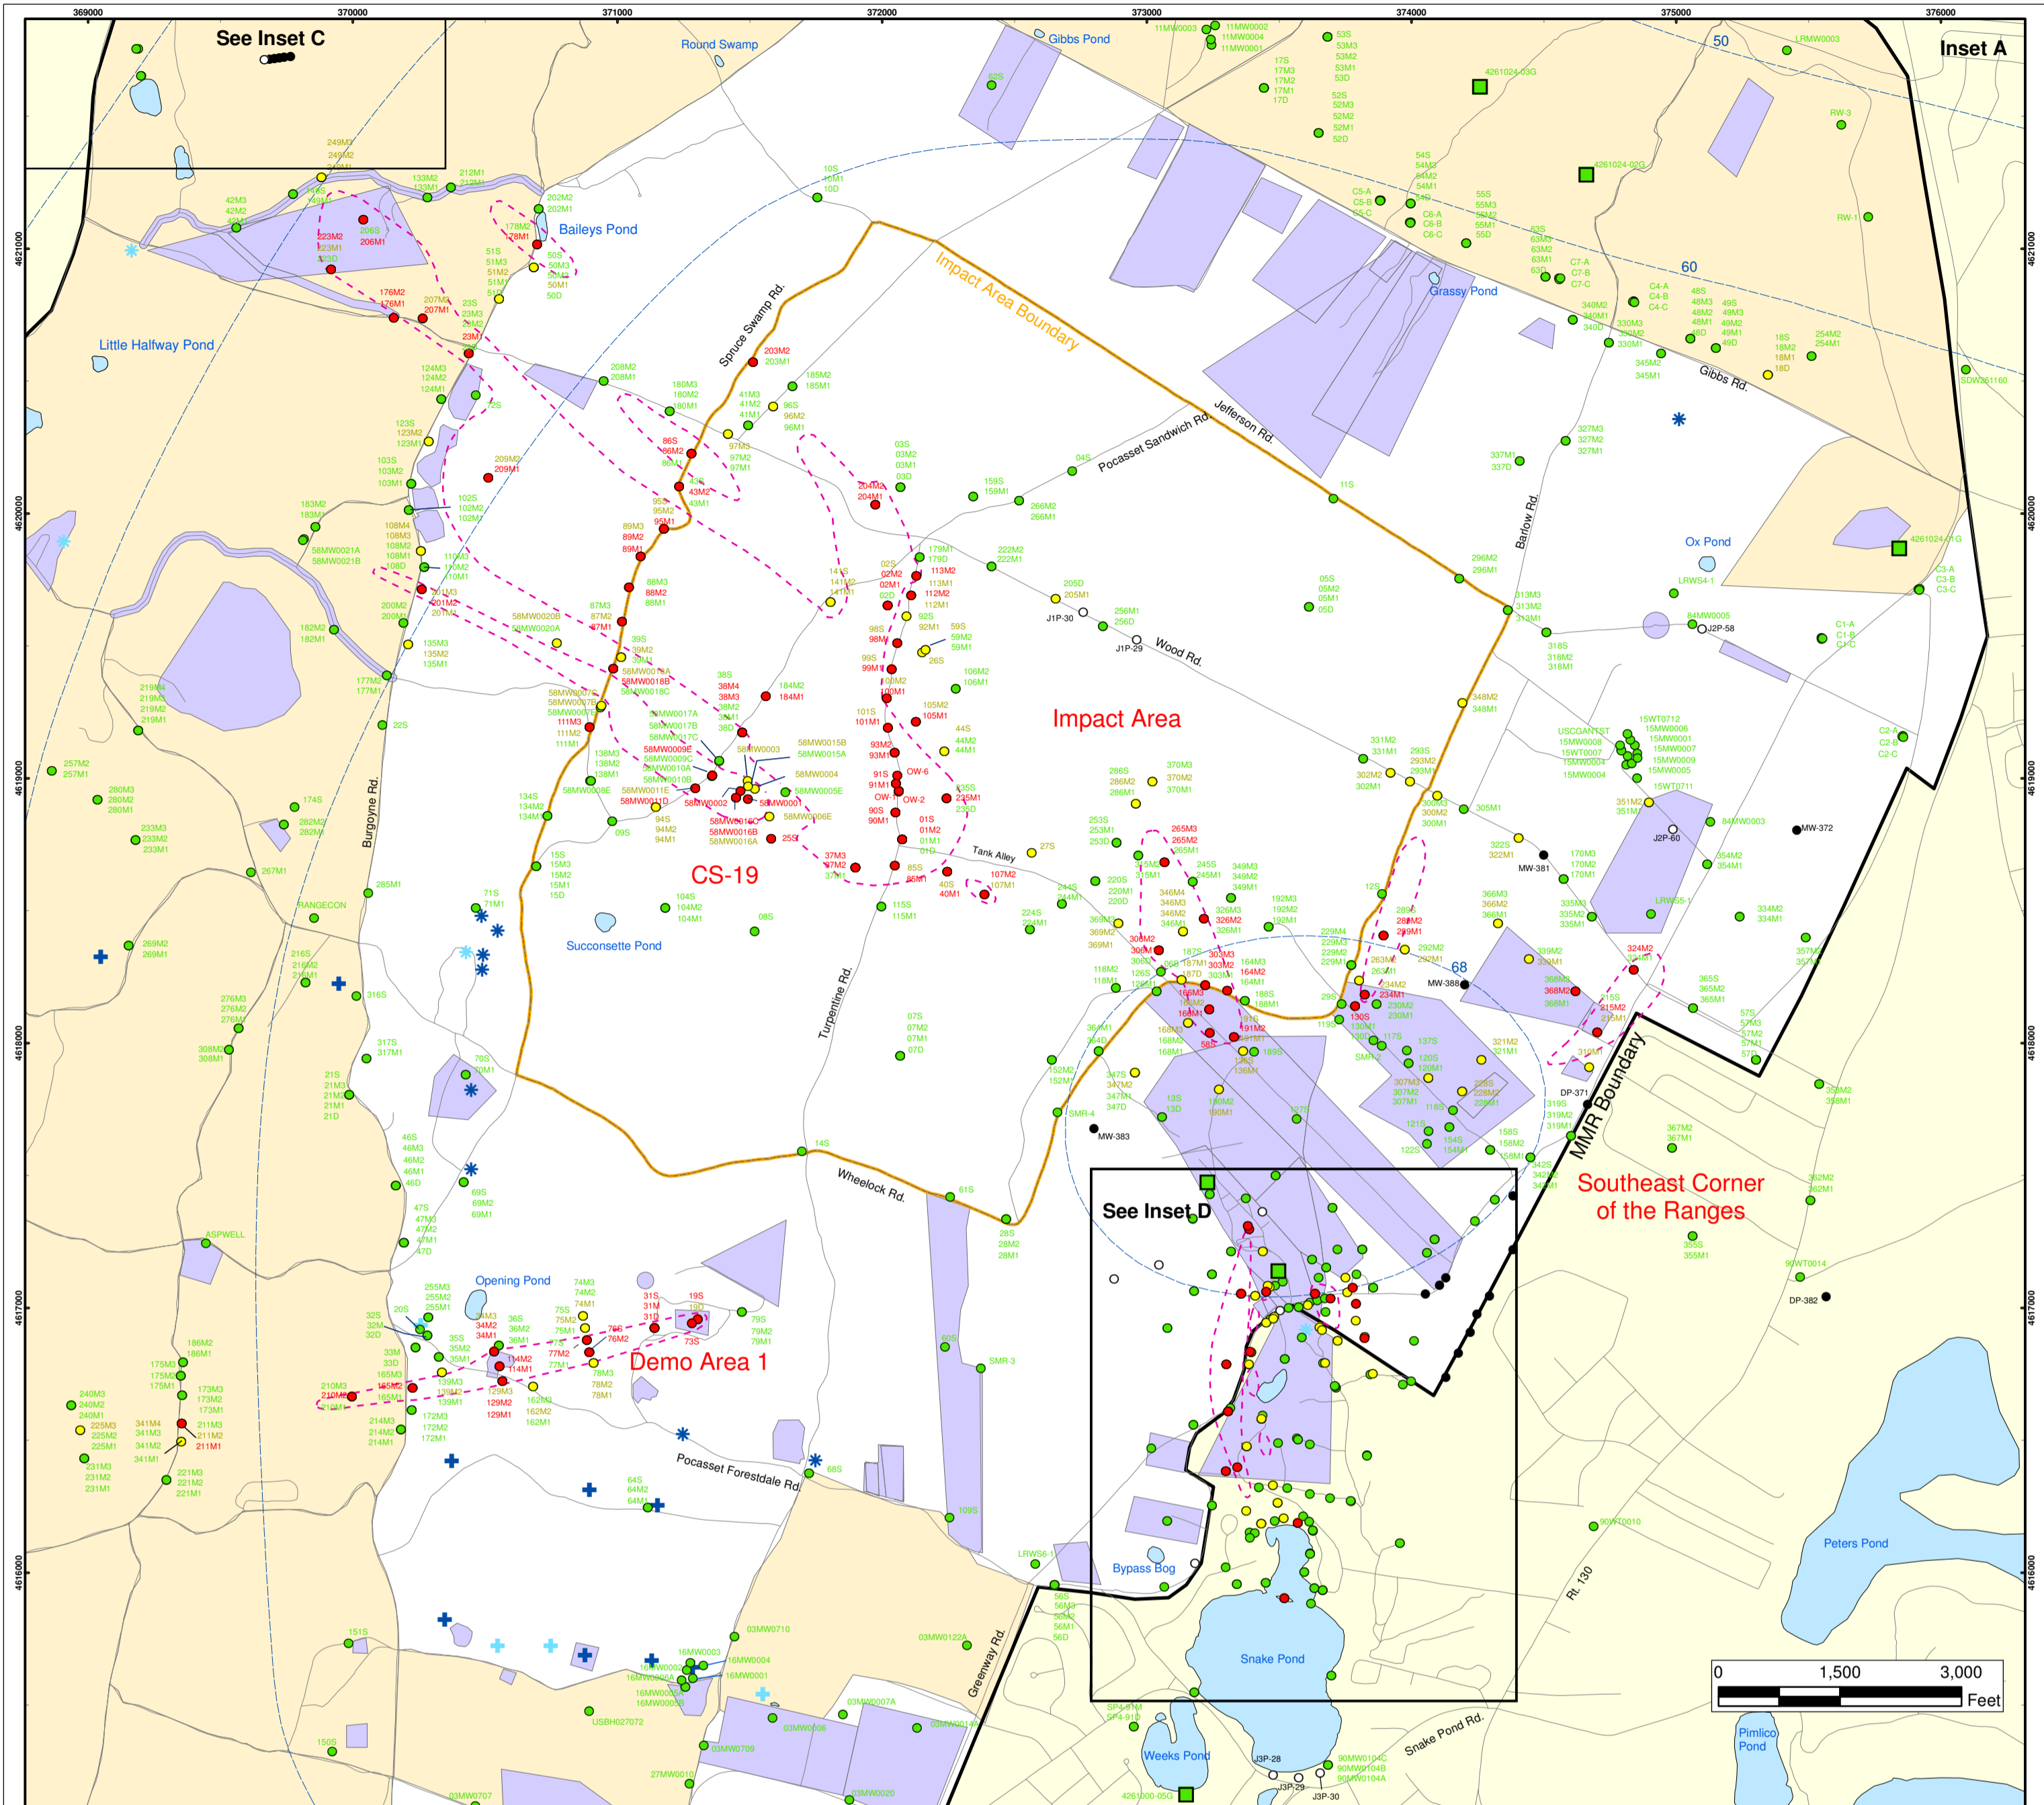

Explosives in Groundwater Compared to Maximum Contaminant Level/Health Advisories



Validated Data as of 08/26/05

- Validated Detection Greater than or Equal to Maximum Contaminant Level/Health Advisories
- Validated Detection Less than Maximum Contaminant Level/Health Advisories
- Validated Non-Detect
- No Data Available
- Proposed Monitoring Well
- Military Training Areas
- Military Ranges
- ⊕ Current Gun Position
- ⊕ Old Gun Position
- ⊕ Old Mortar Position
- Validated Non-Detect Water Supply Well
- Validated Detection Less than Maximum Contaminant Level/Health Advisories Water Supply Well
- Water Table Contour (Feet NGVD), AMEC, September 2003
- Area of RDX Detections Greater than 2.0 ppb
- Central Impact Area 7/15/03
- Demo 1 12/21/04
- SE Ranges (Jacobs Eng.) 10/21/04
- NWC 1/27/05

Impact Area Groundwater Study Program

AMEC Earth & Environmental, Inc.
Westford, Massachusetts

FIGURE 1
Inset Map

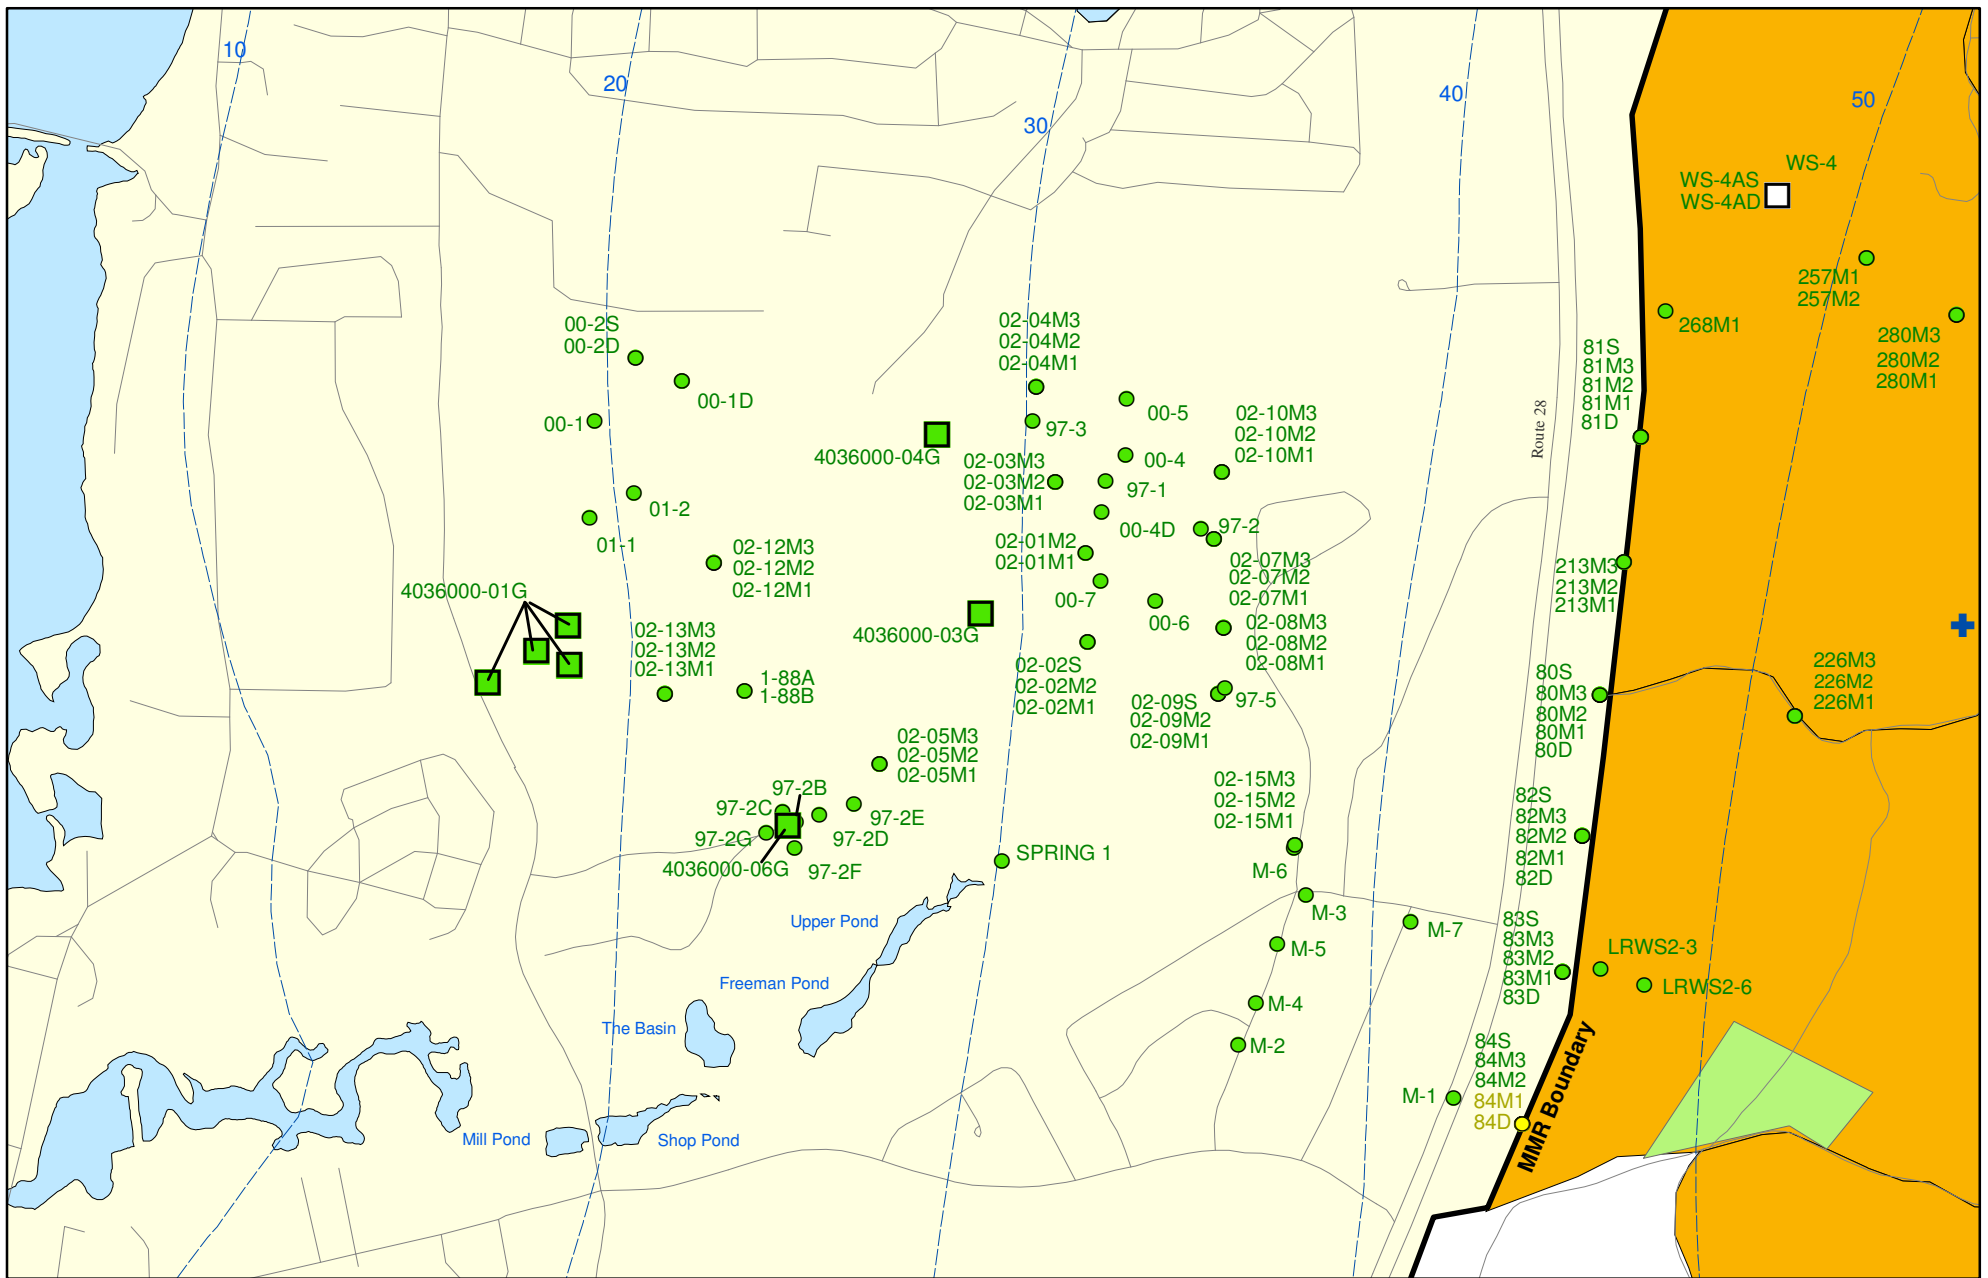


- Validated Detection Less than Maximum Contaminant Level/Health Advisories
- Validated Non-Detect
- + Current Gun Position
- Validated Non-Detect Water Supply Well
- Proposed Water Supply Well
- Combat Training Areas
- Military Training Areas
- Water Table Contour (Feet NGVD)
AMEC, September 2003


Sources & Notes:
 Base map data from US Geological Survey
 7 1/2 minute Topographic maps.
 Source: Office of Geographic and
 Environmental Information (MassGIS)
 Commonwealth of Massachusetts
 Executive Office of Environmental Affairs

AMEC Earth & Environmental, Inc.
 Westford, Massachusetts

**Explosives in Groundwater Compared to
 Maximum Contaminant Level/Health Advisories
 Validated Data as of 08/26/05**







Inset Map B 1

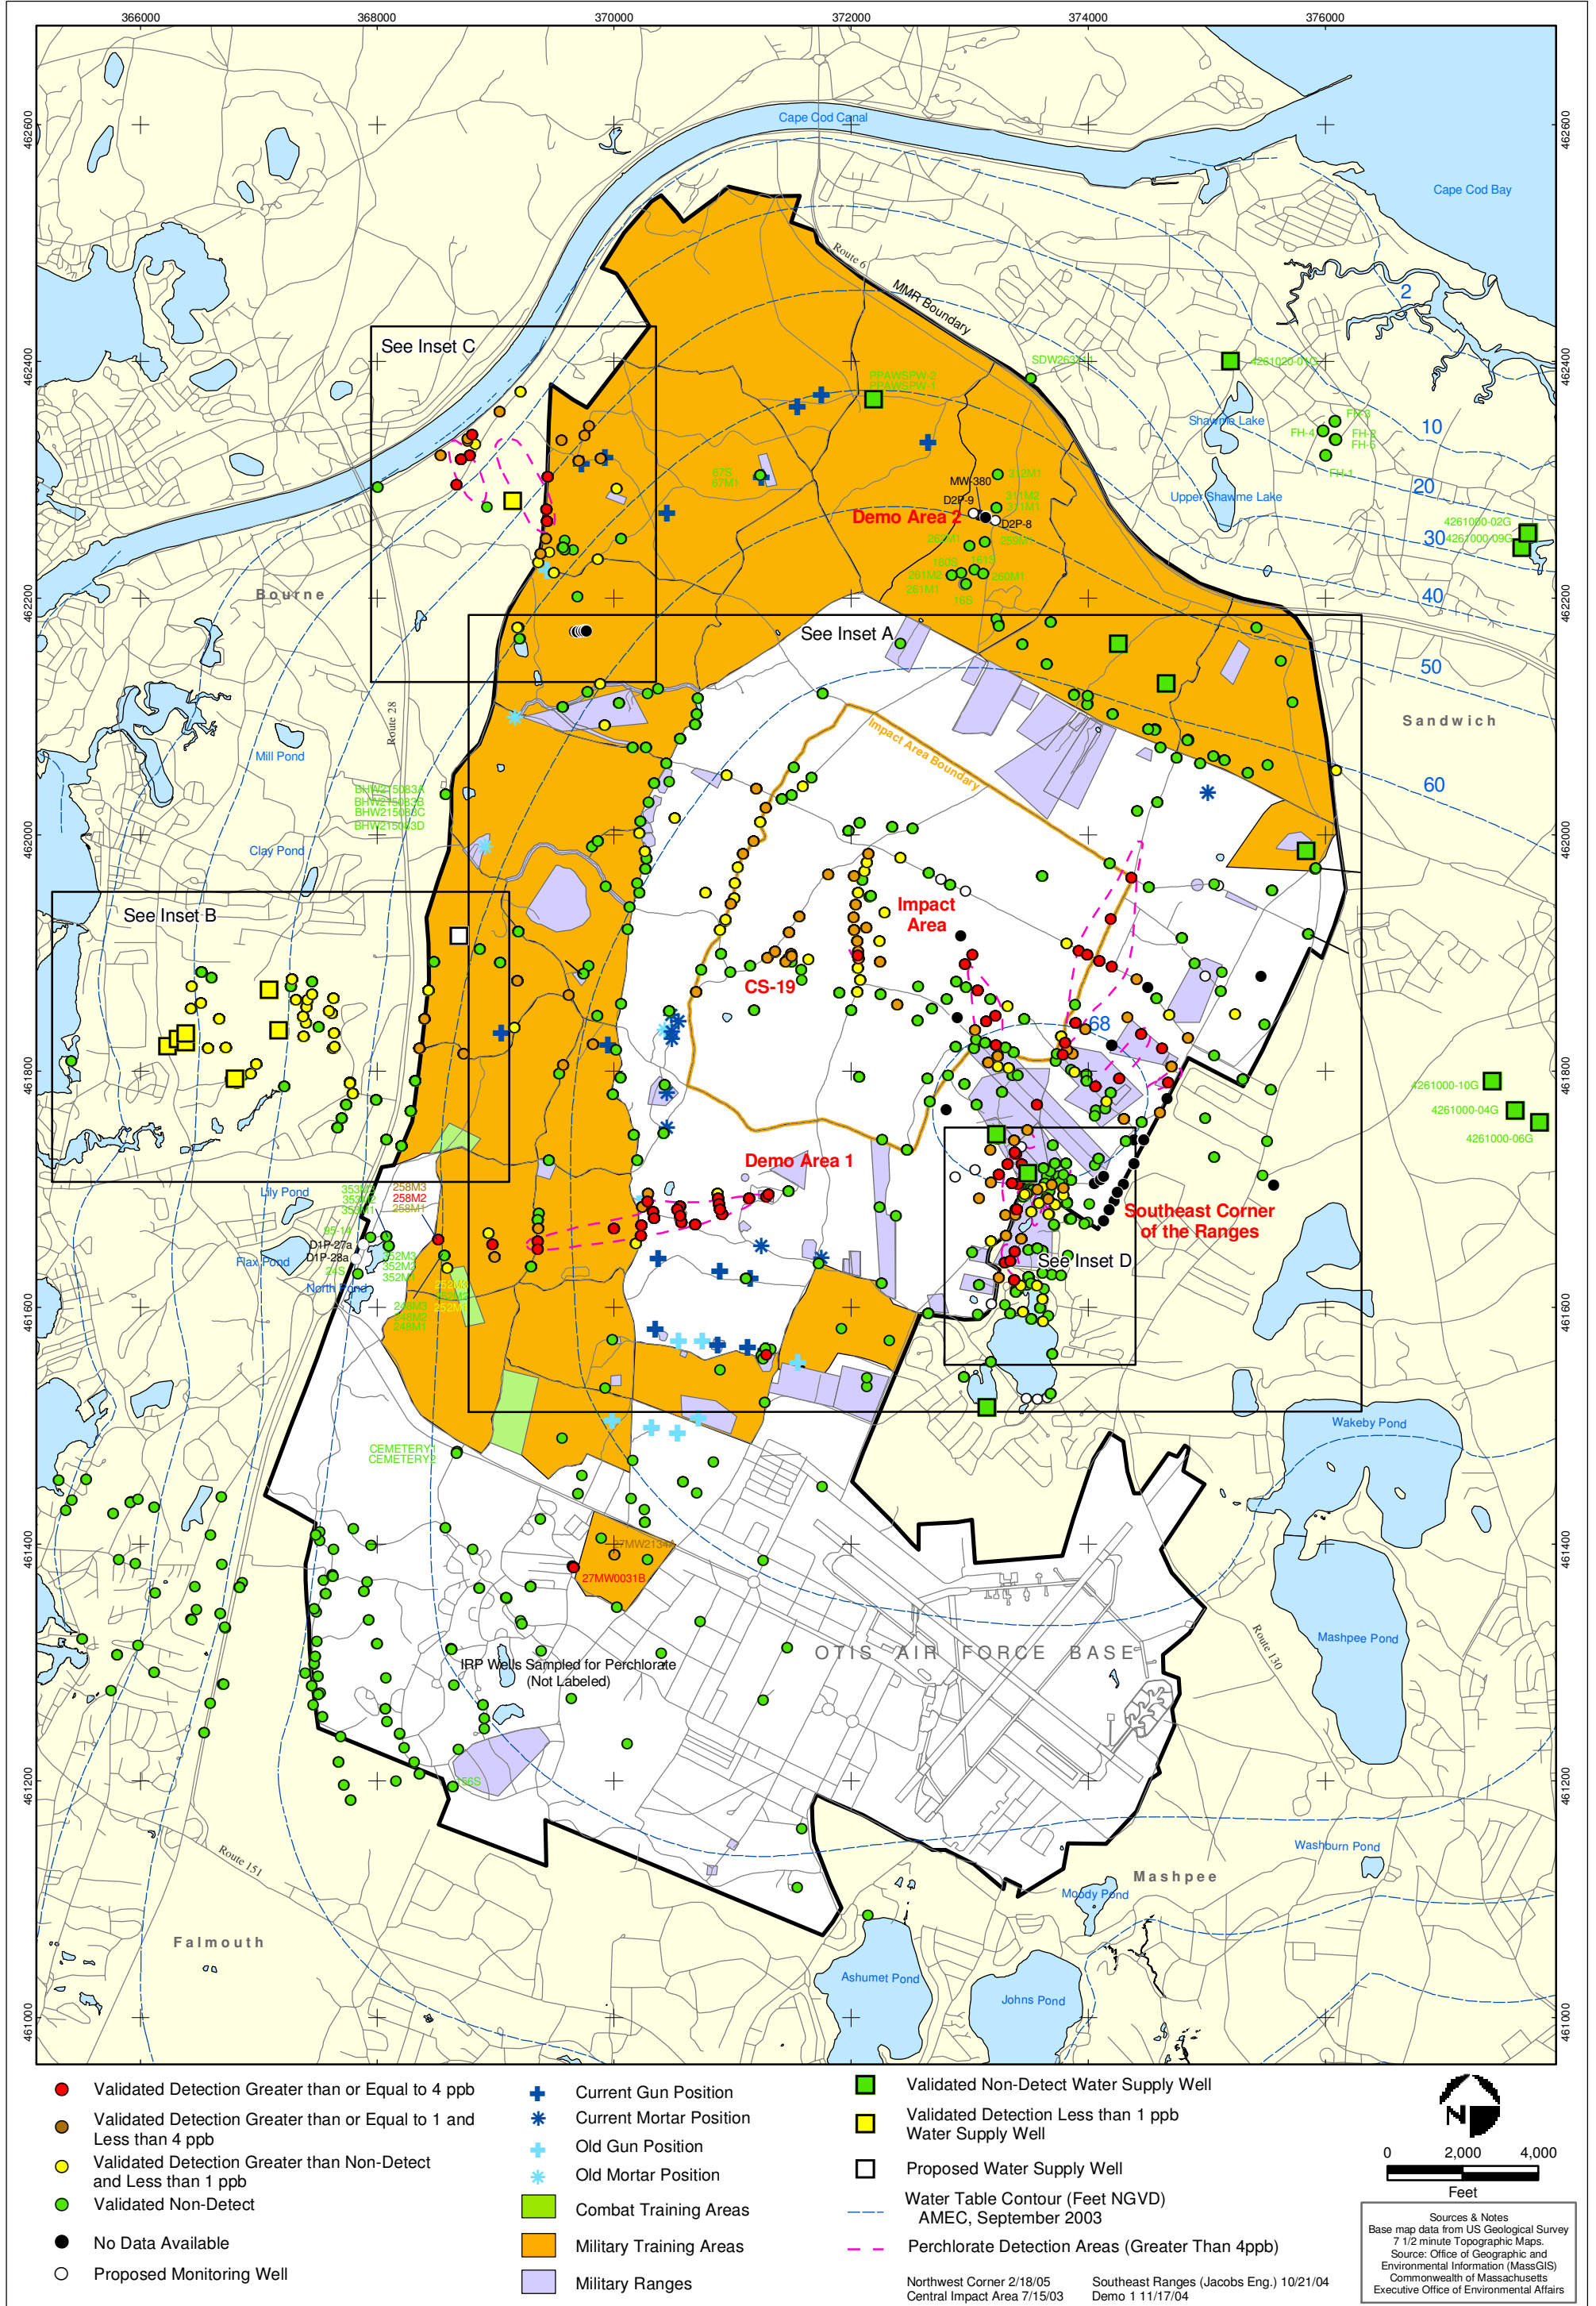

AMEC Earth & Environmental, Inc.
 Westford, Massachusetts

**Perchlorate in Groundwater
 Compared to a 4 ppb Concentration
 Validated Data as of 08/26/05**

J:\GIS\Sept2005\Monthly\perch_overall.pdf
 G:\MMR_COE\Work2005\Monthly\Sept2005\8_Perch\Perch_overall.mxd
 Septmeber 1, 2005 DWN: DNB JBB ABF CHKD: MD

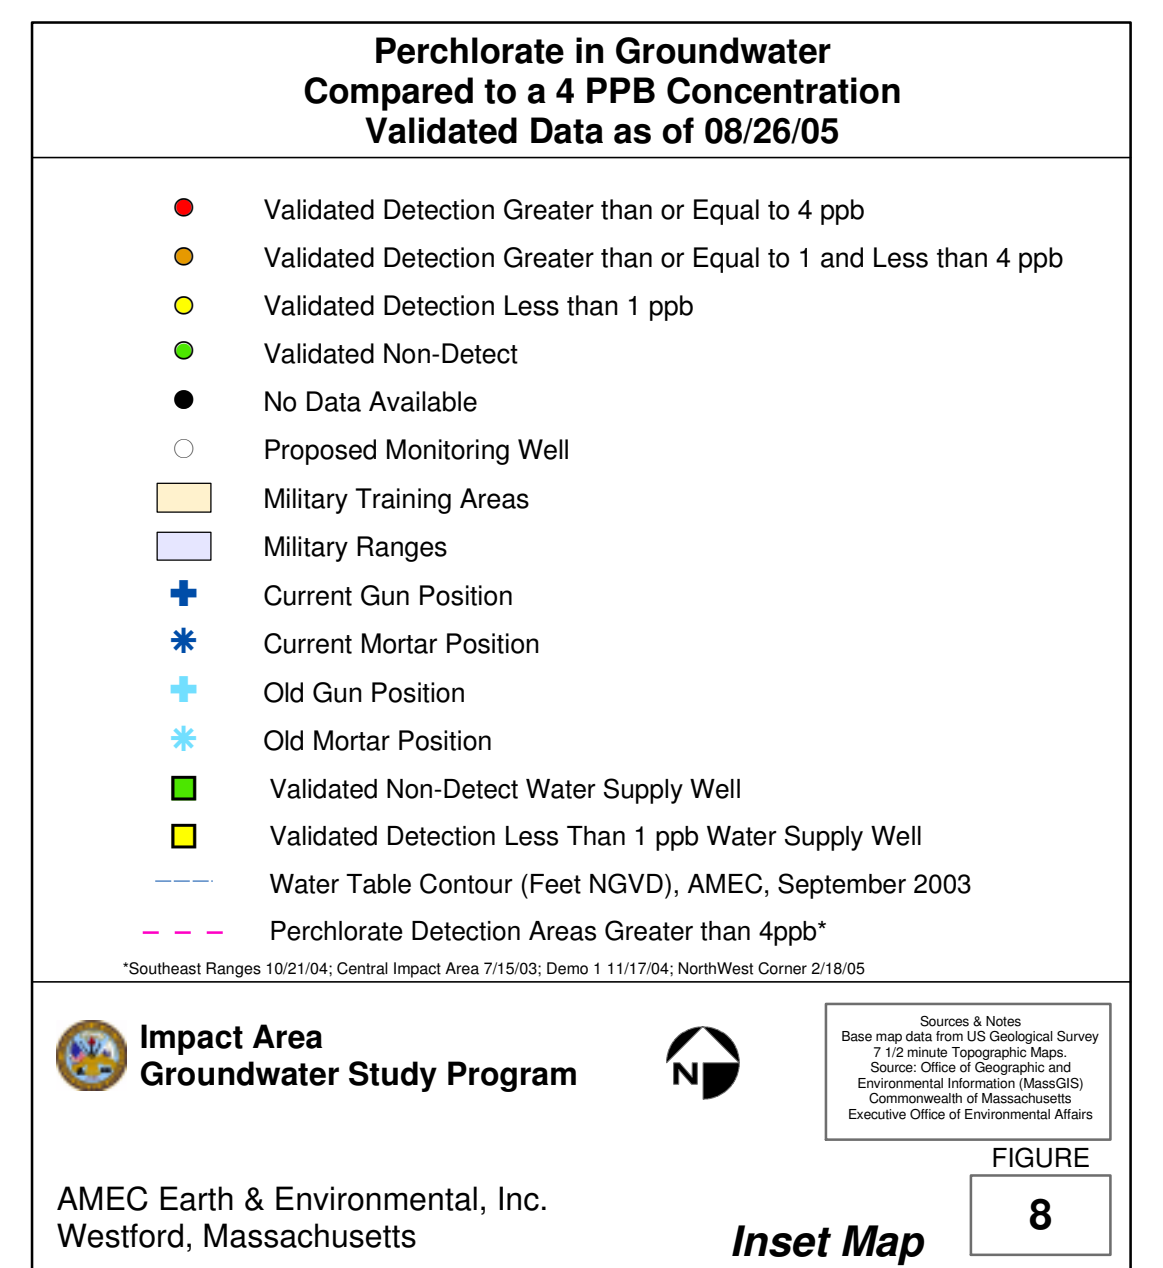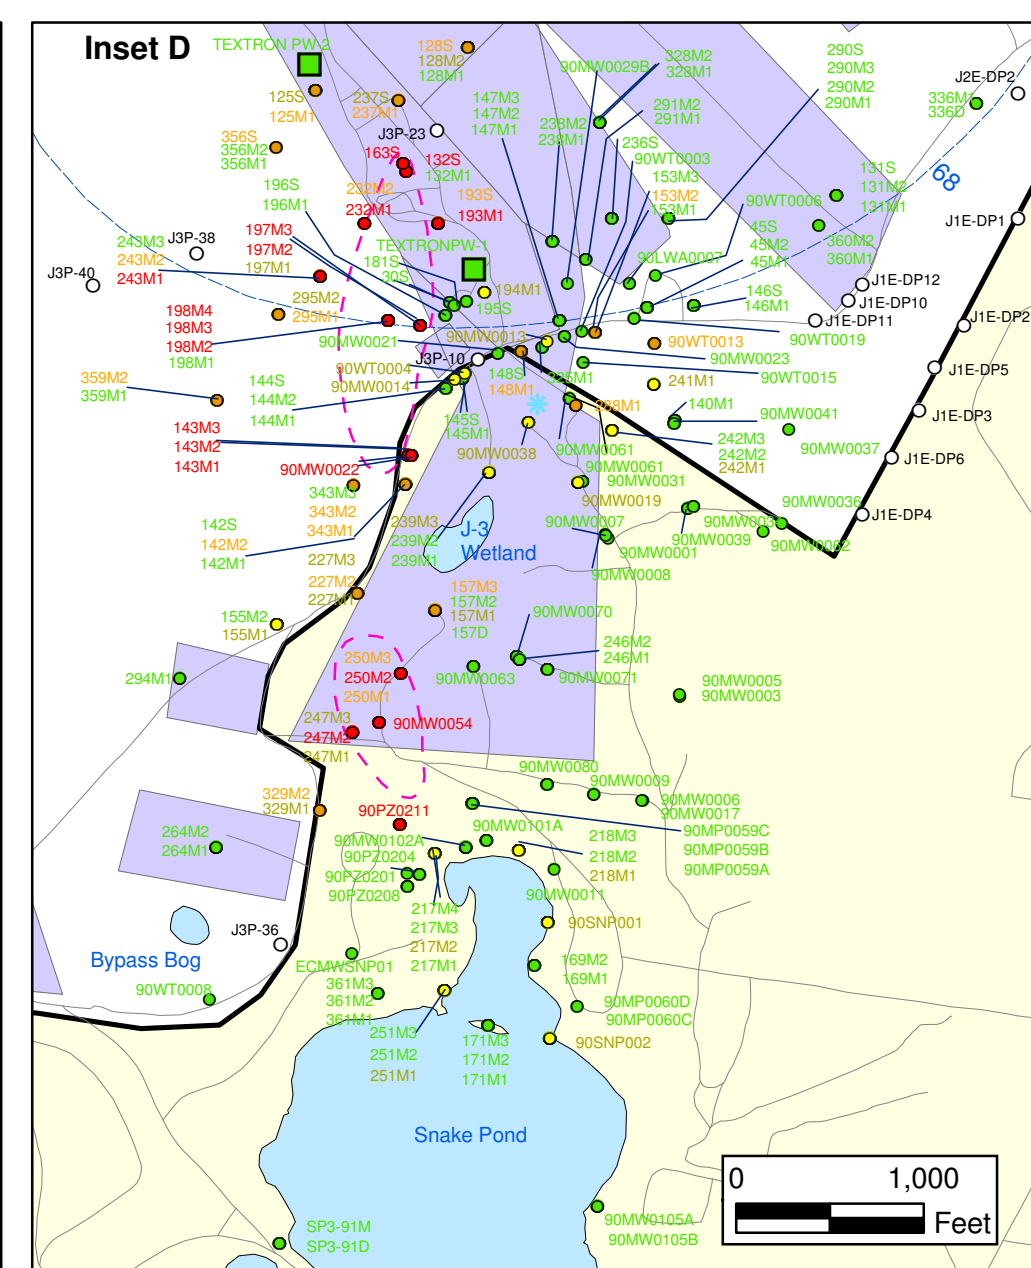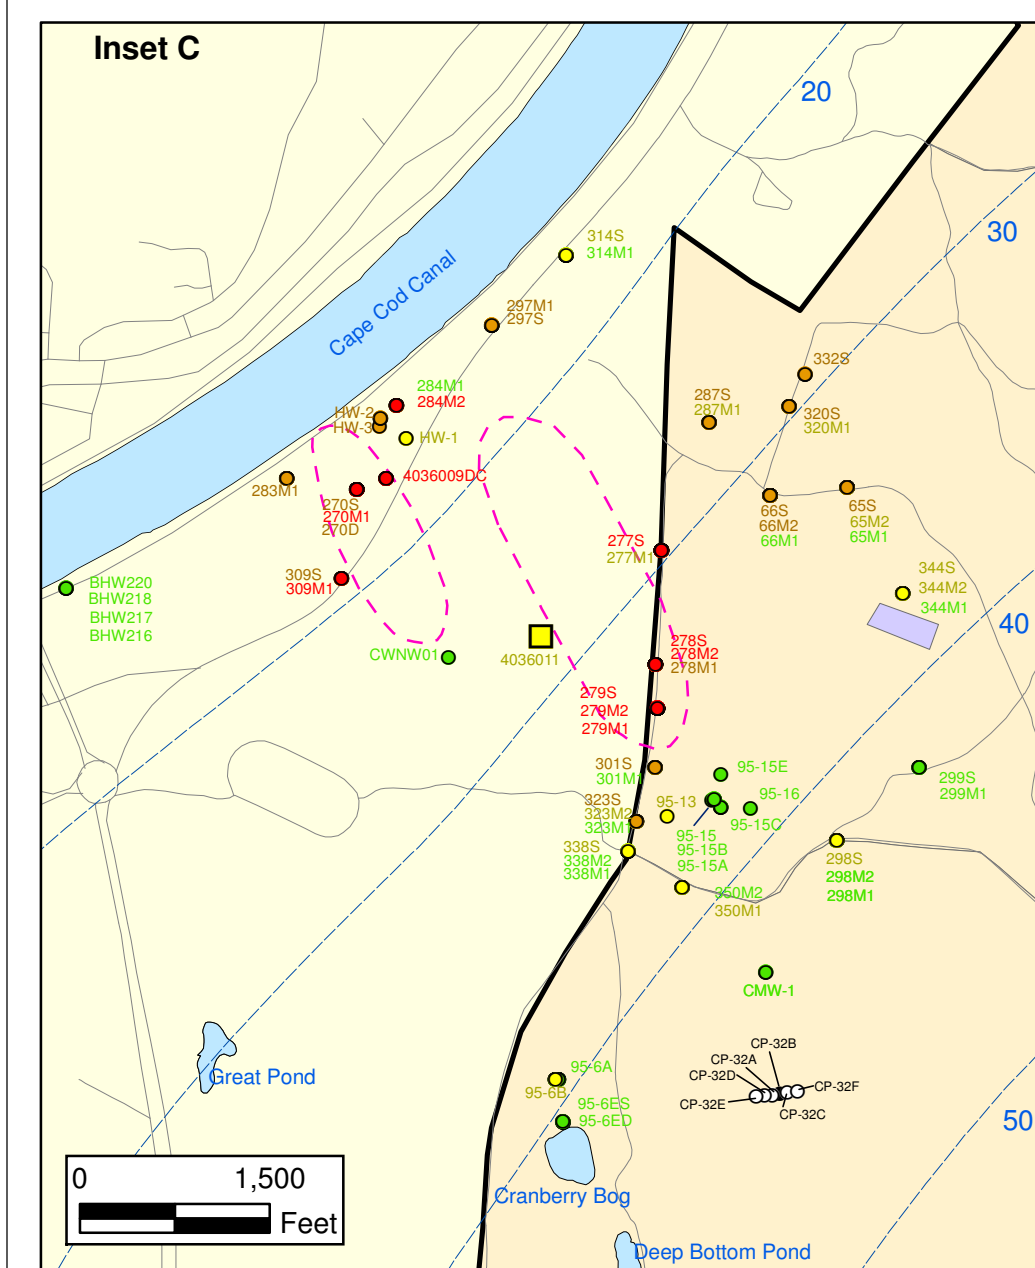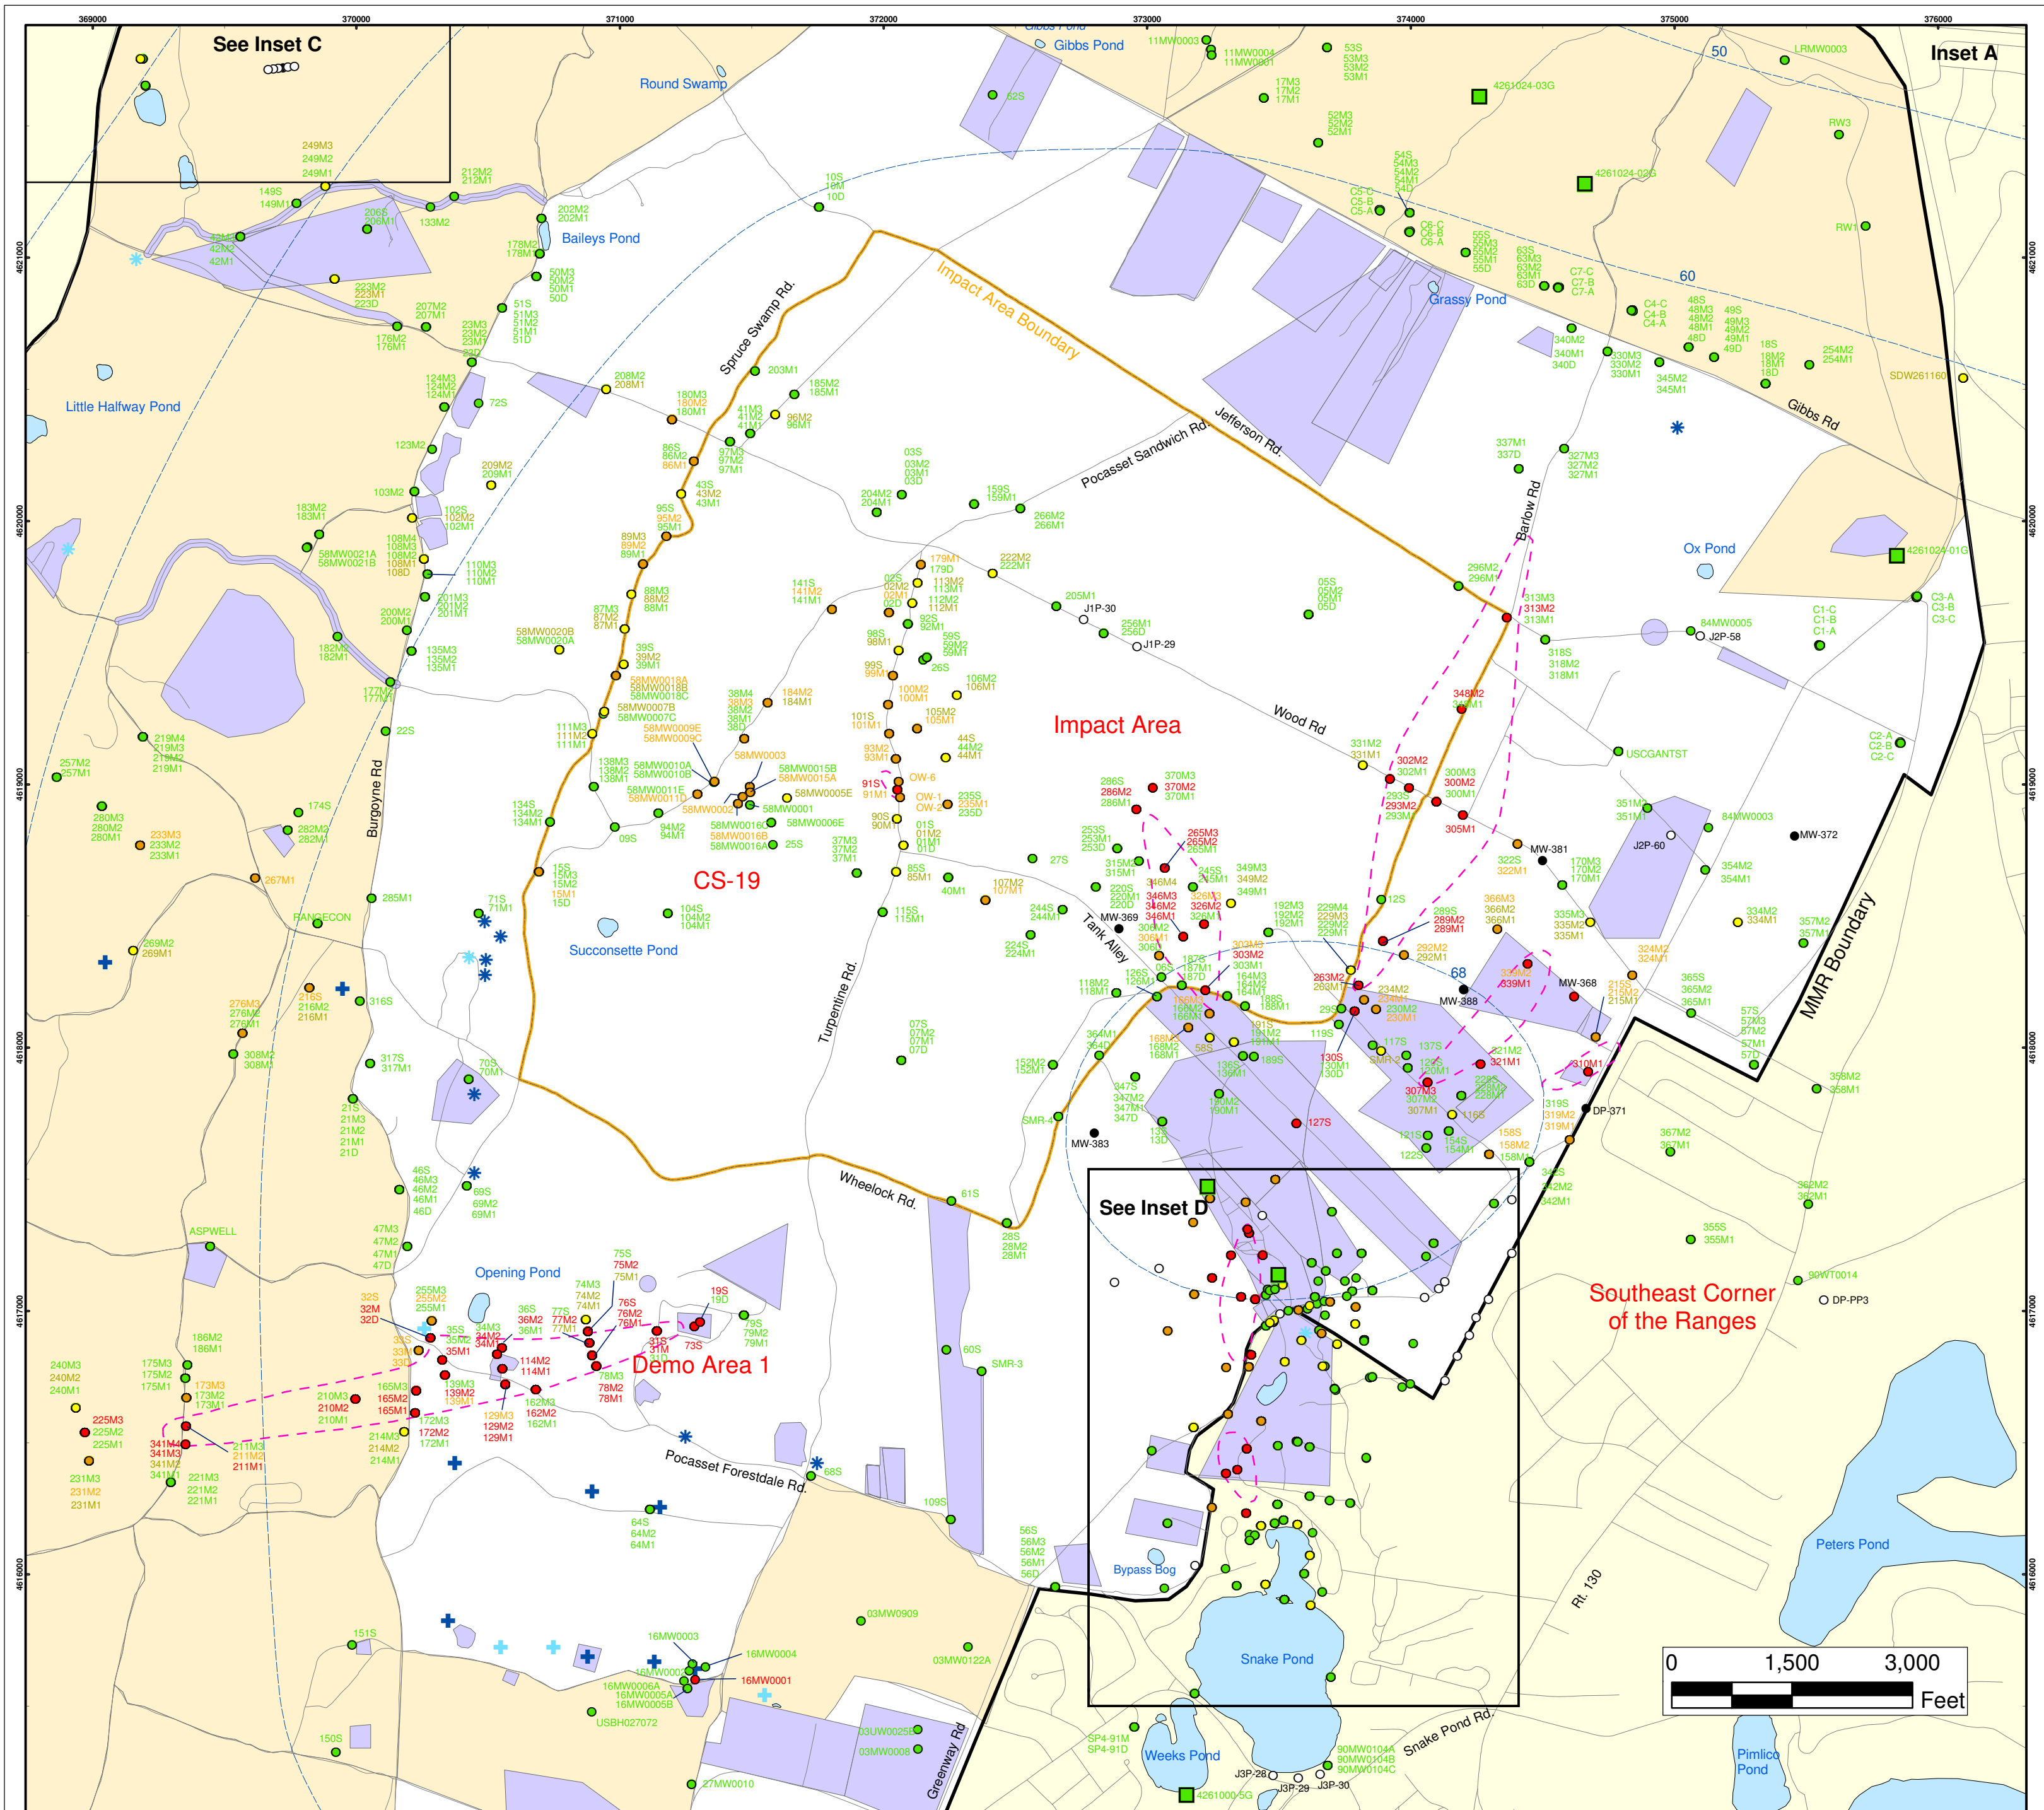

Activity ID	Activity Description	Enforceable Milestone	Orig Dur	Rem Dur	Early Start RCS 52205	Early Finish RCS 52205	Anticipated Start	Anticipated Finish	Variance	2005												2006												2007												2008												2009												2010												
21680	Submit Demo 1 GW Final FS			0	0		11JUL05		19AUG05A	-29																																																																								
Demo 1 Groundwater: Remedy Selection																																																																																		
31520	Prepare Demo 1 GW Remedy Selection Plan			215	0	03SEP04A	15JUL05	08SEP04A	19AUG05A	-25																																																																								
31530	Demo 1 GW Remedy Selection Plan			0	0		15JUL05		19AUG05A	-25																																																																								
31540	Demo 1 GW Public Comment Period			22	22	18JUL05	16AUG05	22AUG05A	21SEP05	-25																																																																								
31550	Demo 1 GW Draft Decision Doc/ Response Summary			5	5	17AUG05	14SEP05	22SEP05	28SEP05	-10																																																																								
31560	EPA Prepare Final Demo1 GW Dec Doc/Response Sum			5	5	15SEP05	05OCT05	28SEP05	05OCT05	0																																																																								
31570	EPA Final Demo 1 GW Decision Doc/ Response Sum.			0	0		05OCT05		05OCT05	0																																																																								
31571	PLACEHOLDER: Demo 1 GW: RD			293	34	01JUL04A	01SEP05	01JUL04A	13OCT05	-28																																																																								
31572	PLACEHOLDER: Demo 1 GW: RA(C)			311	311	02SEP05	01FEB07	03OCT05	29DEC06	23																																																																								
J-1 Range																																																																																		
J-1 Range Soil																																																																																		
J-1 Range Soil: Remedial Investigation																																																																																		
02124	Prepare Final J-1 Geophysical Response Workplan			200*	0*	28OCT04A	07JUL05	28OCT04A	16AUG05A	-28																																																																								
02125	Submit Final J-1 Suppl Geophy Anomaly ResponseWP			0	0		07JUL05		16AUG05A	-28																																																																								
02120	J-1 Geophysical Soil Response			234*	197*	21JUL05	24MAY06	29JUN05A	05JUN06	-7																																																																								
02118	Prepare Draft J-1 Soil RI Report			135*	135*	03MAY06	14NOV06	12MAY06	24NOV06	-7																																																																								
02119	Submit Draft J-1 Soil RI Report	14NOV06		0	0		14NOV06		24NOV06	-7																																																																								
02121	Prepare Final J-1 Soil RI Report			75*	75*	15NOV06	02MAR07	27NOV06	13MAR07	-7																																																																								
02123	Submit Final J-1 Soil RI Report			0	0		02MAR07		13MAR07	-7																																																																								
J-1 Range Soil: Feasibility Study																																																																																		
02128	Scoping Meeting for J-1 Soil FSSR			1	1	15NOV06	15NOV06	27NOV06	27NOV06	-7																																																																								
02129	J-1 Soil FS Screening Report Preparation			60	60	16NOV06	12FEB07	28NOV06	21FEB07	-7																																																																								
02131	Submit Draft J-1 Soil FS Screening Report			0	0		12FEB07		21FEB07	-7																																																																								
02134	Revise J-1 Soil Draft FS Screening Report			75	75	13FEB07	28MAY07	22FEB07	06JUN07	-7																																																																								
02136	Submit Final J-1 Soil FS Screening Report			0	0		28MAY07		06JUN07	-7																																																																								



Activity ID	Activity Description	Enforceable Milestone	Orig Dur	Rem Dur	Early Start RCS 52205	Early Finish RCS 52205	Anticipated Start	Anticipated Finish	Variance	2005 2006 2007 2008 2009 2010											
										02137	Prepare Draft J-1 Soil FS		90	90	01MAY07	04SEP07	10MAY07	13SEP07	-7	[Gantt bar: 10MAY07 - 13SEP07]	
02139	Submit Draft J-1 Soil FS	04SEP07	0	0		04SEP07		13SEP07	-7	[Gantt bar: 10MAY07 - 13SEP07]											
02141	Prepare Final J-1 Soil FS		75*	75*	05SEP07	19DEC07	14SEP07	31DEC07	-7	[Gantt bar: 10MAY07 - 31DEC07]											
02143	Submit Final J-1 Soil FS		0	0		19DEC07		31DEC07	-7	[Gantt bar: 10MAY07 - 31DEC07]											
02166	PLACEHOLDER: J-1 Range Soil: RS/DD		132	132	22NOV07	27MAY08	03DEC07	05JUN08	-7	[Gantt bar: 10MAY07 - 05JUN08]											
J-1 Range Groundwater																					
J-1 Range Groundwater: Remedial Investigation																					
02133	Implement J-1 GW Field Program		478*	150*	30APR04A	22JUL05	30APR04A	29MAR06	-170	[Gantt bar: 30APR04 - 29MAR06]											
02135	Validate J-1 GW Data		500*	172*	30APR04A	23AUG05	30APR04A	28APR06	-170	[Gantt bar: 30APR04 - 28APR06]											
02138	Prepare Draft J-1 GW RI Report		135	135	15JUL05	30JAN06	13MAR06	20SEP06	-163	[Gantt bar: 13MAR06 - 20SEP06]											
02140	Submit Draft J-1 GW RI Report	30JAN06	0	0		30JAN06		20SEP06	-163	[Gantt bar: 13MAR06 - 20SEP06]											
02142	Prepare Final J-1 GW RI Report		75*	75*	31JAN06	16MAY06	21SEP06	10JAN07	-163	[Gantt bar: 13MAR06 - 10JAN07]											
02144	Submit Final J-1 GW RI Report		0	0		16MAY06		10JAN07	-163	[Gantt bar: 13MAR06 - 10JAN07]											
J-1 Range Groundwater: Feasibility Study																					
02145	Scoping Meeting for J-1 GW FSSR		1	1	31JAN06	31JAN06	21SEP06	21SEP06	-163	[Gantt bar: 21SEP06 - 21SEP06]											
02146	J-1 GW FS Screening Report Preparation		30	30	01FEB06	15MAR06	22SEP06	03NOV06	-163	[Gantt bar: 22SEP06 - 03NOV06]											
02147	Submit Draft J-1 GW FS Screening Report		0	0		15MAR06		03NOV06	-163	[Gantt bar: 22SEP06 - 03NOV06]											
02148	Revise J-1 GW Draft FS Screening Report		35	35	16MAR06	03MAY06	06NOV06	27DEC06	-163	[Gantt bar: 22SEP06 - 27DEC06]											
02149	Submit Final J-1 GW FS Screening Report		0	0		03MAY06		27DEC06	-163	[Gantt bar: 22SEP06 - 27DEC06]											
02151	Prepare Draft J-1 GW FS		90	90	07APR06	14AUG06	30NOV06	06APR07	-163	[Gantt bar: 30NOV06 - 06APR07]											
02152	Submit Draft J-1 GW FS	14AUG06	0	0		14AUG06		06APR07	-163	[Gantt bar: 30NOV06 - 06APR07]											
02153	Prepare Final J-1 GW FS		75*	75*	15AUG06	01DEC06	09APR07	23JUL07	-163	[Gantt bar: 30NOV06 - 23JUL07]											
02154	Submit Final J-1 GW FS		0	0		01DEC06		23JUL07	-163	[Gantt bar: 30NOV06 - 23JUL07]											
02164	PLACEHOLDER: J-1 Range GW: RS/DD		132	132	02NOV06	10MAY07	25JUN07	28DEC07	-163	[Gantt bar: 30NOV06 - 28DEC07]											
02174	PLACEHOLDER: J-1 Range GW: RD		260	260	06SEP06	12SEP07	30APR07	01MAY08	-163	[Gantt bar: 30NOV06 - 01MAY08]											
02184	PLACEHOLDER: J-1 Range GW: RA(C)		303	303	13SEP07	17NOV08	02MAY08	07JUL09	-163	[Gantt bar: 30NOV06 - 07JUL09]											

milestone colors
 Milestone > 90 days Out
 Milestone < 90 days Out

Activity ID	Activity Description	Enforceable Milestone	Orig Dur	Rem Dur	Early Start RCS 52205	Early Finish RCS 52205	Anticipated Start	Anticipated Finish	Variance	Timeline												
										2005	2006			2007			2008			2009		
J-2 Range																						
J-2 Range Soil																						
J-2 Range Soil: Remedial Investigation																						
00314	Implement J-2 Geophysical Investig Field Program			381*	227*	12JAN05A	28NOV05	12JAN05A	18JUL06	-160	Implement J-2 Geophysical Investig Field Program											
00325	Prepare Draft J-2 Soil RI Report			135*	135*	03NOV05	18MAY06	29JUN06	12JAN07	-163	Prepare Draft J-2 Soil RI Report											
00327	Submit Draft J-2 Soil RI Report	18MAY06		0	0		18MAY06		12JAN07	-163	Submit Draft J-2 Soil RI Report 163 day delay - revised field program, J-1 priority 1 grids will be investigated prior to J-2 priority 2/3 grids. Increased field duration											
00329	Prepare Final J-2 Soil RI Report			75*	75*	19MAY06	05SEP06	15JAN07	27APR07	-163	Prepare Final J-2 Soil RI Report											
00331	Submit Final J-2 Soil RI Report			0	0		05SEP06		27APR07	-163	Submit Final J-2 Soil RI Report Submittal is 20 Days from MOR Approval											
J-2 Range Soil: RRA																						
03210	Implement J2 Soil RRA Field Program			430*	27*	14JAN04A	13SEP05	14JAN04A	28SEP05	-11	Implement J2 Soil RRA Field Program											
03211	Prepare Draft J-2 Soil RRA Completion of Work Rt			45*	45*	24AUG05	27OCT05	16SEP05	21NOV05	-16	Prepare Draft J-2 Soil RRA Completion of Work Rt											
03212	Submit Draft J-2 Soils RRA Completion of Work Rt	27OCT05		0	0		27OCT05		21NOV05	-16	Submit Draft J-2 Soils RRA Completion of Work Rt 11 day delay - due to extended field program.											
03213	Prepare Final J-2 Soil RRA Completion of Work Rt			75*	75*	28OCT05	16FEB06	22NOV05	13MAR06	-16	Prepare Final J-2 Soil RRA Completion of Work Rt											
03214	Submit Final J-2 Soils RRA Completion of Work Rt			0	0		16FEB06		13MAR06	-16	Submit Final J-2 Soils RRA Completion of Work Rt Submittal is 20 Days from MOR Approval											
J-2 Range Soil: Feasibility Study																						
00332	Scoping Meeting for J-2 Soil FSSR			1	1	19MAY06	19MAY06	15JAN07	15JAN07	-163	Scoping Meeting for J-2 Soil FSSR											
00334	J-2 Soil FS Screening Report Preparation			60	60	22MAY06	15AUG06	16JAN07	09APR07	-163	J-2 Soil FS Screening Report Preparation											
00336	Submit Draft J-2 Soil FS Screening Report			0	0		15AUG06		09APR07	-163	Submit Draft J-2 Soil FS Screening Report											
00338	Revise J-2 Soil Draft FS Screening Report			75	75	16AUG06	04DEC06	10APR07	24JUL07	-163	Revise J-2 Soil Draft FS Screening Report											
00340	Submit Final J-2 Soil FS Screening Report			0	0		04DEC06		24JUL07	-163	Submit Final J-2 Soil FS Screening Report Submittal is 20 Days from MOR Approval											
00342	Prepare Draft J-2 Soil FS			90	90	03NOV06	14MAR07	26JUN07	30OCT07	-163	Prepare Draft J-2 Soil FS											
00344	Submit Draft J-2 Soil FS	14MAR07		0	0		14MAR07		30OCT07	-163	Submit Draft J-2 Soil FS											
00346	Prepare Final J-2 Soil FS			75*	75*	15MAR07	27JUN07	31OCT07	15FEB08	-163	Prepare Final J-2 Soil FS											
00348	Submit Final J-2 Soil FS			0	0		27JUN07		15FEB08	-163	Submit Final J-2 Soil FS Submittal is 20 Days from MOR Approval											
00390	PLACEHOLDER: J-2 Range Soil: RS/DD			132	132	31MAY07	04DEC07	21JAN08	23JUL08	-163	PLACEHOLDER: J-2 Range Soil: RS/DD											
J-2 Range Groundwater																						
J-2 Range Groundwater: Remedial Investigation																						
00347	Implement J-2 GW Field Program			607*	61*	23JUN03A	23JAN06	23JUN03A	17NOV05	43	Implement J-2 GW Field Program Assumes: no additional wells											
00349	Validate J-2 GW Data			552*	83*	09OCT03A	23FEB06	09OCT03A	20DEC05	43	Validate J-2 GW Data											
00351	Prepare Draft J-2 GW RI Report			135	135	04JAN06	17JUL06	15NOV05	30MAY06	33	Prepare Draft J-2 GW RI Report											

Start Date 01FEB03
 Finish Date 20DEC69
 Data Date 21AUG05
 Run Date 25AUG05 08:55

US96
 RCS - by Area w/TARGET bars
 as of 21AUG05
 Sheet 4 of 17

milestone colors
 Milestone > 90 days Out
 Milestone < 90 days Out





Activity ID	Activity Description	Enforceable Milestone	Orig Dur	Rem Dur	Early Start RCS 52205	Early Finish RCS 52205	Anticipated Start	Anticipated Finish	Variance	2005												2006												2007												2008												2009												2010												
00352	Submit Draft J-2 GW RI Report	17JUL06		0	0		17JUL06		30MAY06	33													★ Submit Draft J-2 GW RI Report																																																											
00353	Prepare Final J-2 GW RI Report			75*	75*	18JUL06	01NOV06	31MAY06	14SEP06	33													█ Prepare Final J-2 GW RI Report																																																											
00355	Submit Final J-2 GW RI Report			0	0		01NOV06		14SEP06	33													★ Submit Final J-2 GW RI Report Submittal is 20 Days from MOR Approval																																																											
J-2 Range Groundwater: RRA																																																																																		
00341	Prepare Draft J-2 GW RRA Plan			154*	0*	01NOV04A	26APR05A	01NOV04A	26APR05A	0																																																																								
00381	Submit Draft J-2 GW RRA Plan			0	0		26APR05A		26APR05A	0																																																																								
00391	Prepare Final J-2 GW RRA Plan			139*	58*	27APR05A	31AUG05	27APR05A	14NOV05	-50	█ Prepare Final J-2 GW RRA Plan																																																																							
00401	Submit Final J-2 GW RRA Plan			0	0		31AUG05		14NOV05	-50	★ Submit Final J-2 GW RRA Plan 25 day delay - extended EPA comment duration 25 day delay - extended RCL preparation duration																																																																							
00403	PLACEHOLDER Constr J-2 GW RRA Sys (N.Plume only)			311	311	01SEP05	29SEP06	03OCT05	29DEC06	-61	█ PLACEHOLDER Constr J-2 GW RRA Sys (N.Plume only)																																																																							
00404	System Start Up: J-2 GW RRA Sys (N.Plume only)			0	0		29SEP06		29DEC06	-61	★ System Start Up: J-2 GW RRA Sys (N.Plume only)																																																																							
J-2 Range Groundwater: Feasibility Study																																																																																		
00356	Scoping Meeting for J-2 GW FSSR			1	1	18JUL06	18JUL06	31MAY06	31MAY06	33													Scoping Meeting for J-2 GW FSSR																																																											
00357	J-2 GW FS Screening Report Preparation			30	30	19JUL06	29AUG06	01JUN06	13JUL06	33	█ J-2 GW FS Screening Report Preparation																																																																							
00358	Submit Draft J-2 GW FS Screening Report			0	0		29AUG06		13JUL06	33	★ Submit Draft J-2 GW FS Screening Report																																																																							
00359	Prepare Final J-2 GW Draft FS Screening Report			35	35	30AUG06	19OCT06	14JUL06	31AUG06	33	█ Prepare Final J-2 GW Draft FS Screening Report																																																																							
00360	Submit Final J-2 GW FS Screening Report			0	0		19OCT06		31AUG06	33	★ Submit Final J-2 GW FS Screening Report Submittal is 20 Days from MOR Approval																																																																							
00364	Prepare Draft J-2 GW FS			90	90	22SEP06	01FEB07	07AUG06	14DEC06	33	█ Prepare Draft J-2 GW FS																																																																							
00363	Submit Draft J-2 GW FS	01FEB07		0	0		01FEB07		14DEC06	33	★ Submit Draft J-2 GW FS																																																																							
00365	Prepare Final J-2 GW FS			75*	75*	02FEB07	17MAY07	15DEC06	02APR07	33	█ Prepare Final J-2 GW FS																																																																							
00366	Submit Final J-2 GW FS			0	0		17MAY07		02APR07	33	★ Submit Final J-2 GW FS Submittal is 20 Days from MOR Approval																																																																							
00367	PLACEHOLDER: J-2 Range GW: RS/DD			132	132	20APR07	23OCT07	06MAR07	06SEP07	33	█ PLACEHOLDER: J-2 Range GW: RS/DD																																																																							
00368	PLACEHOLDER: J-2 Range GW: RD			250	250	26JAN07	16JAN08	08DEC06	28NOV07	33	█ PLACEHOLDER: J-2 Range GW: RD																																																																							
00369	PLACEHOLDER: J-2 Range GW: RA(C)			306	306	17JAN08	25MAR09	29NOV07	06FEB09	33	█ PLACEHOLDER: J-2 Range GW: RA(C)																																																																							
J-3 Range																																																																																		
J-3 Range Soils																																																																																		
J-3 Range Soil: Remedial Investigation																																																																																		
02217	Prepare Draft J-3 Soil RI Report			137*	120*	13JUN05	23DEC05	28JUL05A	14FEB06	-34	█ Prepare Draft J-3 Soil RI Report																																																																							
02219	Submit Draft J-3 Soil RI Report	23DEC05		0	0		23DEC05		14FEB06	-34	★ Submit Draft J-3 Soil RI Report 34 day delay - extended RRA EPA comment duration contractor transition																																																																							
02221	Prepare Final J-3 Soil RI Report			75*	75*	27DEC05	13APR06	15FEB06	01JUN06	-34	█ Prepare Final J-3 Soil RI Report																																																																							

Activity ID	Activity Description	Enforceable Milestone	Orig Dur	Rem Dur	Early Start RCS 52205	Early Finish RCS 52205	Anticipated Start	Anticipated Finish	Variance	Timeline												
										2005	2006			2007			2008			2009		
02223	Submit Final J-3 Soil RI Report			0	0		13APR06		01JUN06	-34												
02300	PLACEHOLDER: J-3 Range Soil: FS			287	287	27DEC05	15FEB07	15FEB06	04APR07	-34												
02301	PLACEHOLDER: J-3 Range Soil: RS/DD			132	132	25OCT06	02MAY07	14DEC06	19JUN07	-34												
02302	PLACEHOLDER: J-3 Range Soil: RD			95	95	23JAN07	04JUN07	12MAR07	23JUL07	-34												
02304	PLACEHOLDER: J-3 Range Soil: RA(C)			155	155	05JUN07	11JAN08	24JUL07	28FEB08	-34												
J-3 Range Soil: RRA																						
03306	Implement J-3 Soil RRA Field Program			377*	0*	23FEB04A	10JUN05	23FEB04A		-49												
03307	Prepare Draft J-3 Soil RRA Completion of Work Rt			51*	0*	16MAR05A	25MAY05	16MAR05A	25MAY05A	0												
03308	Submit Draft J-3 Soils RRA Completion of Work Rt	25MAY05		0	0		25MAY05		25MAY05A	0												
03309	Prepare Final J-3 Soils RRA Completion of Wk Rt			103*	43*	26MAY05	12SEP05	26MAY05A	21OCT05	-28												
03310	Submit Final J-3 Soils RRA Completion of Work Rt			0	0		12SEP05		21OCT05	-28												
J-3 Range Groundwater																						
J-3 Range Groundwater: Remedial Investigation																						
02234	Implement J-3 GW Field Program			384*	37*	03APR04A	25AUG05	03APR04A	13OCT05	-33												
02236	Validate J-3 GW Data			336*	72*	01AUG04A	17OCT05	01AUG04A	05DEC05	-33												
02238	Prepare Draft J-3 GW RI Report			135	135	09SEP05	27MAR06	27OCT05	11MAY06	-33												
02240	Submit Draft J-3 GW RI Report	27MAR06		0	0		27MAR06		11MAY06	-33												
02242	Prepare Final J-3 GW RI Report			75	75	28MAR06	12JUL06	12MAY06	28AUG06	-33												
02244	Submit Final J-3 GW RI Report			0	0		12JUL06		28AUG06	-33												
J-3 Range Groundwater: RRA																						
03335	Prepare Final J-3 GW RRA Plan			215*	0*	03MAY04A	14MAR05A	03MAY04A	14MAR05A	0												
03345	Submit Final J-3 GW RRA Plan			0	0		14MAR05A		14MAR05A	0												
03355	Design J-3 GW RRA Treatment System			301*	30*	22JUL04A	03OCT05	22JUL04A	03OCT05	0												
03365	Construct J-3 GW RRA Treatment System			311	311	03OCT05	30JUN06	03OCT05	29DEC06	-124												
J-3/L Range: Groundwater: Feasibility Study																						
02251	J-3/L GW FS Scoping Meeting/Screening Discussion			1	1	14JUN06	14JUN06	01AUG06	01AUG06	-33												
02252	Prepare Draft J-3/L GW FS			90	90	15JUN06	23OCT06	02AUG06	11DEC06	-33												
02253	Submit Draft J-3/L GW FS	23OCT06		0	0		23OCT06		11DEC06	-33												
02255	Prepare Final J-3/L GW FS			75*	75*	24OCT06	09FEB07	12DEC06	28MAR07	-33												

Start Date 01FEB03
 Finish Date 20DEC69
 Data Date 21AUG05
 Run Date 25AUG05 08:55

US96
 Sheet 6 of 17
 RCS - by Area w/TARGET bars
 as of 21AUG05





milestone colors
 Milestone > 90 days Out
 Milestone < 90 days Out

Activity ID	Activity Description	Enforceable Milestone	Orig Dur	Rem Dur	Early Start	Early Finish	Anticipated Start	Anticipated Finish	Variance	Timeline												
										2005	2006			2007			2008			2009		
02257	Submit Final J-3L GW FS			0	0		09FEB07		28MAR07	-33												
02258	PLACEHOLDER: J-3 Range GW: RS/DD			132	132	15JAN07	18JUL07	01MAR07	03SEP07	-33												
02259	PLACEHOLDER: J-3 Range GW: RD			209	209	07NOV06	31AUG07	27DEC06	17OCT07	-33												
02260	PLACEHOLDER: J-3 Range GW: RA(C)			225	225	03SEP07	17JUL08	18OCT07	02SEP08	-33												

L Range


L Range Soils

L Range Soil: Remedial Investigation

02311	Soil Field Investigation L Range			40	0	03NOV03A	15APR05A	03NOV03A	15APR05A	0										
02313	Validate Soil Data L Range			375	0	24NOV03A	16MAY05A	24NOV03A	16MAY05A	0										
02314	Prepare Draft L Soil RI Report			137*	49*	18APR05A	31OCT05	18APR05A	31OCT05	0										
02315	Submit Draft L Soil RI Report	31OCT05		0	0		31OCT05		31OCT05	0										
02316	Prepare Final L Soil RI Report			75*	75*	01NOV05	21FEB06	01NOV05	21FEB06	0										
02317	Submit Final L Soil RI Report			0	0		21FEB06		21FEB06	0										

 Prepare Draft L Soil RI Report







 Submit Draft L Soil RI Report


 Prepare Final L Soil RI Report
FS is not required since soil contaminants are expected to be below risk based levels.


 Submit Final L Soil RI Report
Submittal is 20 Days from MOR Approval

L Range Groundwater

L Range Groundwater: Remedial Investigation

02342	Prepare Final L GW RI Report			191*	35*	08JAN05A	16AUG05	10JAN05A	11OCT05	-38											
02344	Submit Final L GW RI Report			0	0		16AUG05		11OCT05	-38											
0600	Prepare Draft L GW Risk Assessment Report			135	135				12OCT05	26APR06	0										
0602	Submit Draft L GW Risk Assessment Report			0	0					26APR06	0										
0622	Prepare Final L GW Risk Assessment Report			75*	75*				27APR06	11AUG06	0										
0624	Submit Final L GW Risk Assessment Report			0	0					11AUG06	0										


 Prepare Final L GW RI Report

 Submit Final L GW RI Report
Submittal is 20 Days from MOR Approval
2 day delay - extended preparation of RCL
21 day delay - extended EPA review RCL, CRM
15 day delay - awaiting EPA comments of CRM

 Prepare Draft L GW Risk Assessment Report

 Submit Draft L GW Risk Assessment Report





 Prepare Final L GW Risk Assessment Report

 Submit Final L GW Risk Assessment Report


Central Impact Area

CIA Soil


CIA Soil: Remedial Investigation

00261	Prepare Draft CIA Soil RI Report			162	65	04APR04A	01SEP05	04APR04A	23NOV05	-56										
00262	Submit Draft Final CIA Soil RI Report	01SEP05		0	0		01SEP05		23NOV05	-56										
00263	Prepare Final CIA Soil RI Report			75	75	02SEP05	21DEC05	25NOV05	15MAR06	-56										
00292	Submit Final CIA Soil RI Report			0	0		21DEC05		15MAR06	-56										

 Prepare Draft CIA Soil RI Report

 Submit Draft Final CIA Soil RI Report
Schedule will be revised.



 Prepare Final CIA Soil RI Report

 Submit Final CIA Soil RI Report
Submittal is 20 Days from MOR Approval

Activity ID	Activity Description	Enforceable Milestone	Orig Dur	Rem Dur	Early Start RCS 52205	Early Finish RCS 52205	Anticipated Start	Anticipated Finish	Variance	Timeline												
										2005	2006			2007			2008			2009		
CIA Soil: Focused Investigation																						
03011	Field Investigations Soil FI		97	28	19NOV03A	30JUN05	19NOV03A	15MAY06	-218	Field Investigations Soil FI												
03014	Lab Analysis/Data Validation Soil FI		144	68	26DEC03A	26AUG05	26DEC03A	12JUL06	-218	Lab Analysis/Data Validation Soil FI												
03021	Revise Draft Report Soil FI		65	60	17NOV04A	23NOV05	17NOV04A	05OCT06	-218	Revise Draft Report Soil FI Awaiting Agency Comments												
03023	Submit Revised Draft Report Soil FI	23NOV05	0	0		23NOV05		05OCT06	-218	★ Submit Revised Draft Report Soil FI 218 days delay - extended field program (2) rounds of Lysimeter sampling 9/05 & 4/06.												
03024	Prepare Final Report Soil FI		75	75	25NOV05	15MAR06	06OCT06	25JAN07	-218	Prepare Final Report Soil FI												
03025	Submit Final Report Soil FI		0	0		15MAR06		25JAN07	-218	★ Submit Final Report Soil FI Submittal is 20 Days from MOR Approval												
CIA Soil: RRA Targets 23/42																						
03119	RRA Implementation		434	0	14JAN04A	15JUN05	14JAN04A	30JUN05A	-11													
03120	Prepare Draft CIA Completion of Work Targ 23/42		46*	0*	16JUN05	18AUG05	15JUN05A	18AUG05A	0	Prepare Draft CIA Completion of Work Targ 23/42												
03121	Submit Draft CIA Completion of Work Rpt 42 & 23	18AUG05	0	0		18AUG05		18AUG05A	0	★ Submit Draft CIA Completion of Work Rpt 42 & 23												
03122	Prepare Final Draft CIA Compl of Wk Target 23/42		75*	74*	19AUG05	07DEC05	19AUG05A	07DEC05	0	Prepare Final Draft CIA Compl of Wk Target 23/42												
03123	Submit Final CIA Completion of WkRt Target 23/42		0	0		07DEC05		07DEC05	0	★ Submit Final CIA Completion of WkRt Target 23/42 Submittal is 20 Days from MOR Approval												
Treatability Study																						
03083	Treatability Study		648*	469*	06DEC04A	04OCT06	06DEC04A	29JUN07	-187	Treatability Study (Includes Technologies for CIA and Gun & Mortar Positions)												
CIA Soil & GW: Feasibility Study																						
22398	Model FS Screening Report Scenarios		124	32	16JUN03A	30AUG05	16JUN03A	05OCT05	-25	Model FS Screening Report Scenarios												
22110	CIA Soil & GW FS Screening Report Preparation		124*	34*	14APR05A	07OCT05	14APR05A	07OCT05	0	CIA Soil & GW FS Screening Report Preparation												
22120	Submit Draft CIA Soil & GW FS Screening Report	07OCT05	0	0		07OCT05		07OCT05	0	★ Submit Draft CIA Soil & GW FS Screening Report Schedule to be revised after scoping mt w/Agency												
22130	Prepare Final CIA Draft Soil & GW FS Screen Rpt		75	75	11OCT05	30JAN06	11OCT05	30JAN06	0	Prepare Final CIA Draft Soil & GW FS Screen Rpt												
22140	Submit Final CIA Soil & GW FS Screening Report		0	0		30JAN06		30JAN06	0	★ Submit Final CIA Soil & GW FS Screening Report Submittal is 20 days from MOR Approval												
22143	Prepare Draft Post Screen Invest CIA Source Area WP		124*	0*			14JUN05A	15AUG05A	0	Prepare Draft Post Screen Invest CIA Source Area WP												
22145	Submit Draft Post Screen Invest CIA Source Area WP		0	0				15AUG05A	0	★ Submit Draft Post Screen Invest CIA Source Area WP Schedule to be revised after scoping mt w/Agency												
22146	Prepare Final Post Screen Invest CIA Source Area WP		76*	72*			16AUG05A	05DEC05	0	Prepare Final Post Screen Invest CIA Source Area WP												
22148	Submit Final Post Screen Invest CIA Source Area WP		0	0				05DEC05	0	★ Submit Final Post Screen Invest CIA Source Area WP												
22150	PLACEHOLDER: Post Screening Invest CIA Field Prgm		223	223			06DEC05	24OCT06	0	PLACEHOLDER: Post Screening Invest CIA Field Prgm												
22210	Prepare Draft CIA Soil & GW FS		135	135	15FEB06	07MAY07	25OCT06	07MAY07	0	Prepare Draft CIA Soil & GW FS												
22220	Submit Draft CIA Soil & GW FS	07MAY07	0	0		07MAY07		07MAY07	0	★ Submit Draft CIA Soil & GW FS												
22230	Prepare Final CIA Soil & GW FS		105	105	08MAY07	02OCT07	08MAY07	02OCT07	0	Prepare Final CIA Soil & GW FS												

Start Date 01FEB03
 Finish Date 20DEC69
 Data Date 21AUG05
 Run Date 25AUG05 08:55

US96
 Sheet 8 of 17
 RCS - by Area w/TARGET bars
 as of 21AUG05

milestone colors
 Milestone > 90 days Out
 Milestone < 90 days Out

Activity ID	Activity Description	Enforceable Milestone	Orig Dur	Rem Dur	Early Start RCS 52205	Early Finish RCS 52205	Anticipated Start	Anticipated Finish	Variance	Timeline (2005-2010)														
										2005	2006			2007			2008			2009			2010	
22240	Submit Final CIA Soil & GW FS			0	0		02OCT07		02OCT07	0														
CIA Soil & GW: Remedy Selection																								
32505	CIA Soil & GW RS Plan Scoping Meeting			1	1	08MAY07	08MAY07	08MAY07	08MAY07	0														
32510	Prepare Draft CIA Soil & GW Remedy Selection Plan			60	60	09MAY07	01AUG07	09MAY07	01AUG07	0														
32520	Revise Draft CIA Soil & GW Remedy Selection Plan			75	75	02AUG07	15NOV07	02AUG07	15NOV07	0														
32530	Submit CIA Soil & GW Remedy Selection Plan	15NOV07		0	0		15NOV07		15NOV07	0														
32540	CIA Soil & GW Public Comment Period for RS			21	21	16NOV07	14DEC07	16NOV07	14DEC07	0														
32550	Draft CIA Soil & GW Decision Doc/ Resp Summary			64	64	17DEC07	17MAR08	17DEC07	17MAR08	0														
32560	EPA Prepare CIA Final Draft Dec Doc/Response Sum			20	20	18MAR08	14APR08	18MAR08	14APR08	0														
32570	EPA Submit CIA Final Decision Doc/ Response Sum			0	0		14APR08		14APR08	0														
32571	PLACEHOLDER: CIA Soil: RD			303	303	05SEP07	06NOV08	05SEP07	06NOV08	0														
32578	PLACEHOLDER: CIA Soil: RA(C)			758	758	07NOV08	20OCT11	07NOV08	20OCT11	0														
CIA Groundwater																								
CIA Groundwater: Remedial Investigation																								
02030	Prepare Final CIA GW Report			417*	59*	19MAR04A	15AUG05	19MAR04A	15NOV05	-63														
02035	Submit Final CIA GW Rpt Addendum (TM 01-6)			0	0		15AUG05		15NOV05	-63														
32579	PLACEHOLDER: CIA GW: RD			261	261	03OCT07	07OCT08	03OCT07	07OCT08	0														
32580	PLACEHOLDER: CIA GW: RA(C)			427	427	08OCT08	07JUN10	08OCT08	07JUN10	0														
Western Boundary																								
Western Boundary																								
Western Boundary: Remedial Investigation																								
03473	Prepare Western Boundary Draft RI Report			363*	33*	28APR04A	06OCT05	28APR04A	06OCT05	0														
03483	Submit Western Boundary Draft RI Report	06OCT05		0	0		06OCT05		06OCT05	0														
03494	Prepare Final Western Boundary RI Report			75	75	07OCT05	27JAN06	07OCT05	27JAN06	0														
03495	Submit Final Western Boundary RI Report			0	0		27JAN06		27JAN06	0														
Northwest Corner																								
Northwest Corner																								
Northwest Corner: Remedial Investigation																								
03443	Air Dispersion Model			116*	5*	16MAR05A	29JUL05	16MAR05A	26AUG05	-20														
03444	Prepare Draft Northwest Corner RI Rpt			135*	121*	02AUG05	15FEB06	02AUG05A	15FEB06	0														

milestone colors

- Milestone > 90 days Out
- Milestone < 90 days Out

Activity ID	Activity Description	Enforceable Milestone	Orig Dur	Rem Dur	Early Start RCS 52205	Early Finish RCS 52205	Anticipated Start	Anticipated Finish	Variance	Timeline												
										2005	2006			2007			2008			2009		
NW1150	Submit Draft Northwest Corner RI Rpt	15FEB06		0	0		15FEB06		15FEB06	0												
03446	Prepare Final Northwest Corner RI Rpt			75	75	16FEB06	02JUN06	16FEB06	02JUN06	0												
03448	Submit Final Northwest Corner RI Rpt			0	0		02JUN06		02JUN06	0												
Northwest Corner: Feasibility Study																						
03450	Northwest Corner FS Scoping Meeting			1	1	05MAY06	05MAY06	05MAY06	05MAY06	0												
03451	Prepare Draft Northwest Corner FS			135	135	08MAY06	17NOV06	08MAY06	17NOV06	0												
03452	Submit Draft Northwest Corner FS	17NOV06		0	0		17NOV06		17NOV06	0												
03453	Prepare Final Northwest Corner FS			75	75	20NOV06	07MAR07	20NOV06	07MAR07	0												
03454	Submit Final Northwest Corner FS			0	0		07MAR07		07MAR07	0												
03455	PLACEHOLDER: NWC RSDD			88	88	08FEB07	11JUN07	08FEB07	11JUN07	0												
Demo 2																						
Demo 2 Soil																						
Demo 2 Soil: RRA																						
01540	Prepare Draft Demo 2 RRA Completion of Work Rpt			65	0	09DEC04A	31MAY05	09DEC04A	31MAY05A	0												
01541	Submit Draft Demo 2 RRA Completion of Work	31MAY05		0	0		31MAY05		31MAY05A	0												
01580	Prepare Final Draft Demo 2 RRA Completion Wk Rpt			105*	48*	01JUN05	15SEP05	01JUN05A	29OCT05	-30												
01590	Submit Final Demo 2 RRA Completion of Work			0	0		15SEP05		29OCT05	-30												
Demo 2 Groundwater																						
Demo 2 Groundwater: Remedial Investigation																						
01544	Prepare Final Demo 2 GW RI Workplan			75	0	10FEB05A	02AUG05	10FEB05A	02AUG05A	0												
01545	Submit Final Demo 2 GW RI Workplan			0	0		02AUG05		02AUG05A	0												
01564	Implement Demo 2 RI Field Program			97*	51*	15JUN05	06OCT05	16JUN05A	02NOV05	-18												
01565	Lab Analysis Data Validation Demo 2			56*	56*	25JUL05	08NOV05	15SEP05	06DEC05	-18												
01558	Prepare Draft Demo 2 GW RI Report			135	135	20SEP05	05APR06	17OCT05	01MAY06	-18												
01559	Submit Draft Demo 2 GW RI Report	05APR06		0	0		05APR06		01MAY06	-18												
01561	Prepare Final Demo 2 GW RI Report			75	75	06APR06	21JUL06	02MAY06	16AUG06	-18												
01562	Submit Final Demo 2 GW RI Report			0	0		21JUL06		16AUG06	-18												
Demo 2 Groundwater: Feasibility Study																						
01563	Scoping Meeting for Demo 2 GW FSSR			1	1	06APR06	06APR06	02MAY06	02MAY06	-18												

Start Date 01FEB03
 Finish Date 20DEC69
 Data Date 21AUG05
 Run Date 25AUG05 08:55

US96
 Sheet 10 of 17
 RCS - by Area w/TARGET bars
 as of 21AUG05

milestone colors
 Milestone > 90 days Out
 Milestone < 90 days Out

Activity ID	Activity Description	Enforceable Milestone	Orig Dur	Rem Dur	Early Start RCS 52205	Early Finish RCS 52205	Anticipated Start	Anticipated Finish	Variance	2005												2006												2007												2008												2009												2010												
00553	Revise G&M GW RI Report			75	75	28DEC06	12APR07	28DEC06	12APR07	0																																																																								
00554	Submit Final G&M GW RI Report			0	0		12APR07		12APR07	0																																																																								

Former A Range

Former A Range

Former A Range: Remedial Investigation

01584	Field Investigation Former A Range			56	29	28OCT04A	07JUL05	28OCT04A	30SEP05	-60	
01585	Receive/Validate Former A Range Data			50	68	26NOV04A	30AUG05	26NOV04A	29NOV05	-61	
01586	Prepare Former A Range RI Report			135	135	13JUL05	26JAN06	07OCT05	24APR06	-61	
01587	Submit Draft Former A Range RI Report	26JAN06		0	0		26JAN06		24APR06	-61	
01588	Prepare Final Draft Former A Range RI Report			75	75	27JAN06	12MAY06	25APR06	09AUG06	-61	
01589	Submit Final Former A Range RI Report			0	0		12MAY06		09AUG06	-61	
01702	PLACEHOLDER: Former A: FSSR/FS			331	331	27JAN06	17MAY07	25APR06	13AUG07	-61	

Former A: RRA


01610	Prepare Draft Former A RRA Work Plan			30	30	03OCT05*	15NOV05	03OCT05*	15NOV05	0	
01612	Submit Draft Former A RRA Work Plan	15NOV05		0	0		15NOV05		15NOV05	0	
01614	Prepare Final Former A RRA Work Plan			75	75	16NOV05	07MAR06	16NOV05	07MAR06	0	
01617	Submit Final Former A RRA Work Plan			0	0		07MAR06		07MAR06	0	
01618	PLACEHOLDER: Implement Former A RRA Field Program			44	44	07FEB06	10APR06	07FEB06	10APR06	0	
01619	Prepare Draft Former A RRA Completion of Work Rt			45	45	11APR06	13JUN06	11APR06	13JUN06	0	
01620	Submit Draft Former A RRA Completion of Work Rt	13JUN06		0	0		13JUN06		13JUN06	0	
01621	Prepare Final Former A RRA Completion of Work Rt			75	75	14JUN06	28SEP06	14JUN06	28SEP06	0	
01622	Submit Final Former A RRA Completion of Work Rt			0	0		28SEP06		28SEP06	0	

Former K Range

Former K Range

Former K Range: Remedial Investigation

01506	Field Investigation Former K			15	0	11AUG04A	15APR05A	11AUG04A	15APR05A	0	
01507	Receive/Validate Former K Data			45	0	31AUG04A	13JUN05	31AUG04A	13JUN05A	0	
01508	Prepare Former K Range RI Report			50	52	02MAY05A	03NOV05	02MAY05A	03NOV05	0	
01509	Submit Draft Former K Range RI Report	03NOV05		0	0		03NOV05		03NOV05	0	

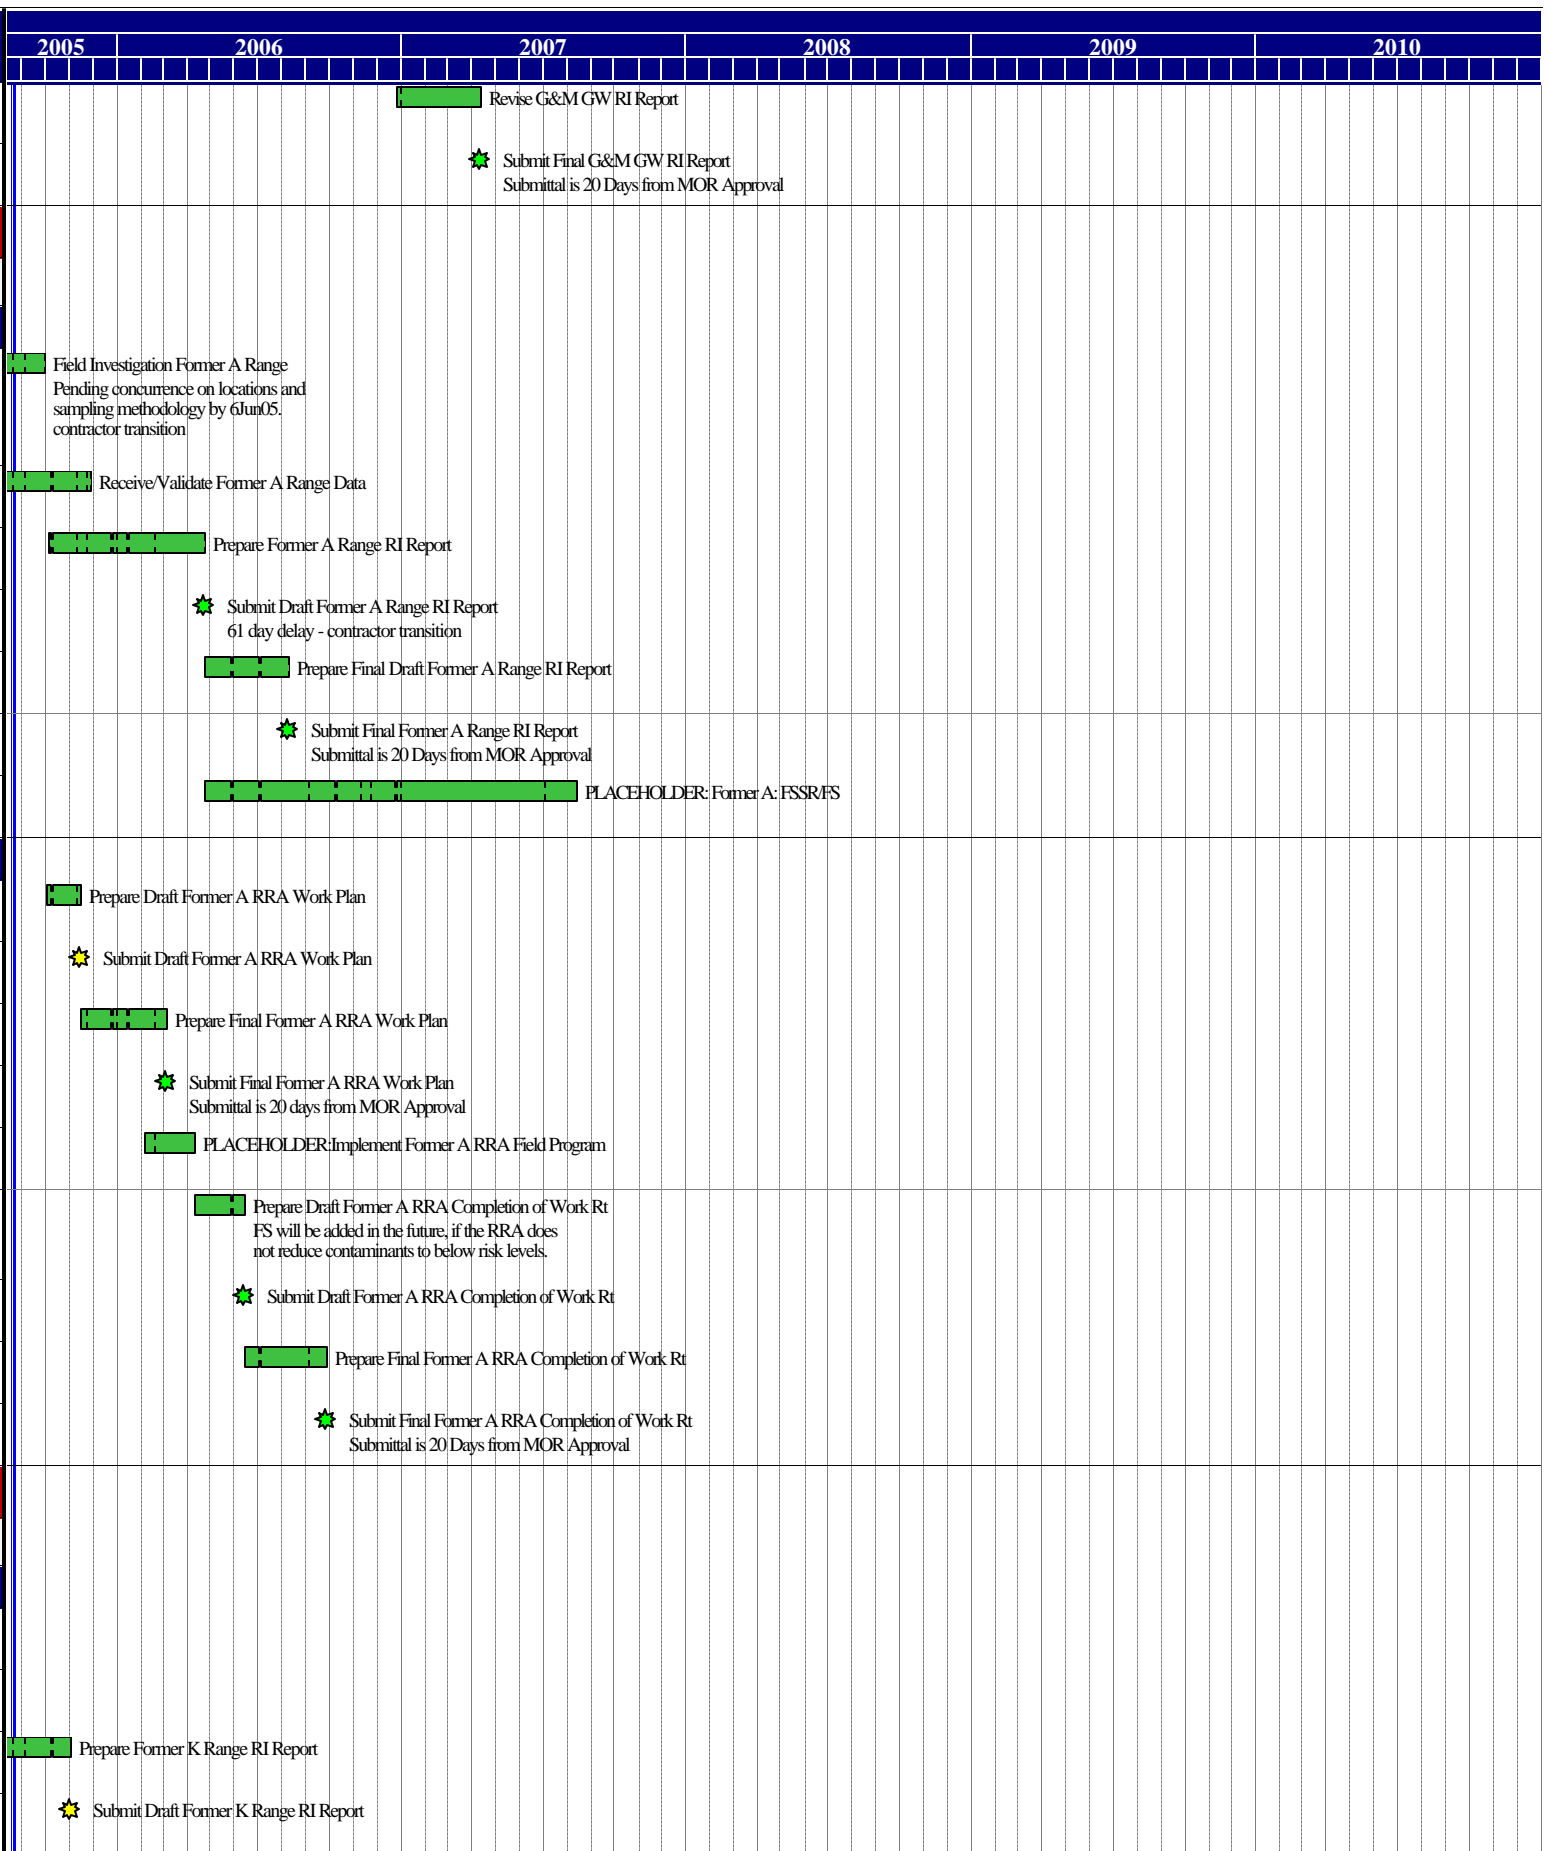

milestone colors

- Milestone > 90 days Out
- Milestone < 90 days Out

Activity ID	Activity Description	Enforceable Milestone	Orig Dur	Rem Dur	Early Start RCS 52205	Early Finish RCS 52205	Anticipated Start	Anticipated Finish	Variance	2005												2006												2007												2008												2009												2010												
01510	Prepare Final Draft Former K Range RI Report			75	75	04NOV05	24FEB06	04NOV05	24FEB06	0													Prepare Final Draft Former K Range RI Report																																																											
01511	Submit Final Former K Range RI Report			0	0		24FEB06		24FEB06	0																																																																								
01720	PLACEHOLDER: Former K: FSSR/FS			331	331	04NOV05	01MAR07	04NOV05	01MAR07	0													PLACEHOLDER: Former K: FSSR/FS																																																											
Former K: RRA																																																																																		
01512	Prepare Draft Former K RRA Work Plan			30	30	03OCT05*	15NOV05	03OCT05*	15NOV05	0													Prepare Draft Former K RRA Work Plan																																																											
01513	Submit Draft Former K RRA Work Plan	15NOV05		0	0		15NOV05		15NOV05	0																																																																								
01514	Prepare Final Former K RRA Work Plan			75	75	16NOV05	07MAR06	16NOV05	07MAR06	0													Prepare Final Former K RRA Work Plan																																																											
01515	Submit Final Former K RRA Work Plan			0	0		07MAR06		07MAR06	0																																																																								
01516	PLACEHOLDER: Implement Former K RRA Field Program			45	45	07FEB06	11APR06	07FEB06	11APR06	0													PLACEHOLDER: Implement Former K RRA Field Program																																																											
01517	Prepare Draft Former K RRA Completion of Work Rt			45	45	12APR06	14JUN06	12APR06	14JUN06	0													Prepare Draft Former K RRA Completion of Work Rt FS will be added in the future, if the RRA does not reduce contaminants to below risk levels.																																																											
01518	Submit Draft Former K RRA Completion of Work Rt	14JUN06		0	0		14JUN06		14JUN06	0																																																																								
01519	Prepare Final Former K RRA Completion of Work Rt			75	75	15JUN06	29SEP06	15JUN06	29SEP06	0													Prepare Final Former K RRA Completion of Work Rt																																																											
01520	Submit Final Former K RRA Completion of Work Rt			0	0		29SEP06		29SEP06	0																																																																								
Phase II B																																																																																		
Phase II (b)																																																																																		
Phase II (b): Remedial Investigation																																																																																		
01560	Prepare Final 2b RI Report			726*	121*	01APR03A	14NOV05	01APR03A	15FEB06	-63													Prepare Final 2b RI Report FS is not currently scheduled since soil contaminants are expected to be below risk based levels.																																																											
01570	Submit Final Phase 2b RI Rpt (TM 02-6)			0	0		14NOV05		15FEB06	-63																																																																								
Long Term Monitoring																																																																																		
Groundwater Monitoring Programs																																																																																		
08376	Prepare Annual LTGM Draft Sampling Plan for 2005			52	0	03JAN05A	08APR05A	03JAN05A	08APR05A	0																																																																								
08377	Submit Annual LTGM Draft Sampling Plan for 2005			0	0		08APR05A		08APR05A	0																																																																								
08384	Prepare Final Annual LTGM Sampling Plan 2005			81*	0*	11APR05A	07OCT05	11APR05A	03AUG05A	46																																																																								
08387	Submit Final Annual LTGM Sampling Plan for 2005			0	0		07OCT05		03AUG05A	46													Submit Final Annual LTGM Sampling Plan for 2005																																																											
Ammunition Supply Point																																																																																		
Ammunition Supply Point																																																																																		
Ammunition Supply Point: RRA																																																																																		
00900	Prepare Draft ASP RRA Work Plan			32	32	03OCT05*	17NOV05	03OCT05*	17NOV05	0													Prepare Draft ASP RRA Work Plan																																																											

Activity ID	Activity Description	Enforceable Milestone	Orig Dur	Rem Dur	Early Start RCS 52205	Early Finish RCS 52205	Anticipated Start	Anticipated Finish	Variance	2005												2006												2007												2008												2009												2010												
00901	Submit Draft ASP RRA Work Plan	17NOV05		0	0		17NOV05		17NOV05	0	★ Submit Draft ASP RRA Work Plan																																																																							
00902	Prepare Final ASP RRA Work Plan			75	75	18NOV05	09MAR06	18NOV05	09MAR06	0	■ Prepare Final ASP RRA Work Plan																																																																							
00903	Submit Final ASP RRA Work Plan			0	0		09MAR06		09MAR06	0	★ Submit Final ASP RRA Work Plan Submittal is 20 Days from MOR Approval																																																																							
00904	PLACEHOLDER: Implement ASP RRA Field Program			75	75	09FEB06	25MAY06	09FEB06	25MAY06	0	■ PLACEHOLDER: Implement ASP RRA Field Program																																																																							
00909	Lab Analysis Data Validation ASP RRA			80	80	02MAR06	22JUN06	02MAR06	22JUN06	0	■ Lab Analysis Data Validation ASP RRA																																																																							
00905	Prepare Draft ASP RRA Completion of Work Rt			45	45	23JUN06	25AUG06	23JUN06	25AUG06	0	■ Prepare Draft ASP RRA Completion of Work Rt FS is not currently scheduled since soil contaminants are expected to be below risk based levels.																																																																							
00906	Submit Draft ASP RRA Completion of Work Rt	25AUG06		0	0		25AUG06		25AUG06	0	★ Submit Draft ASP RRA Completion of Work Rt																																																																							
00907	Prepare Final ASP RRA Completion of Work Rt			75	75	28AUG06	14DEC06	28AUG06	14DEC06	0	■ Prepare Final ASP RRA Completion of Work Rt																																																																							
00908	Submit Final ASP RRA Completion of Work Rt			0	0		14DEC06		14DEC06	0	★ Submit Final ASP RRA Completion of Work Rt Submittal is 20 Days from MOR Approval																																																																							

BA-1 Training Area

BA-1 Training Area

BA-1 Training Area: RRA

BA0050	BA-1 Soil Conduct Field Program			5	0			13JUN05A	18JUL05A	0																																																																								
BA0100	BA-1 Soil Compile Data & Submit to Agency			5	0			19JUL05A	26JUL05A	0																																																																								
BA0110	Agency Review/Approve Completion Data BA-1 RRA			15	5			27JUL05A	26AUG05	0	■ Agency Review/Approve Completion Data BA-1 RRA																																																																							
BA0115	Backfill Excavation: BA-1 Training Area			7	7			29AUG05*	07SEP05	0	■ Backfill Excavation: BA-1 Training Area																																																																							
BA0130	Prepare Draft BA-1 Soil Letter Rpt (COWR)			45	45			08SEP05	10NOV05	0	■ Prepare Draft BA-1 Soil Letter Rpt (COWR)																																																																							
BA0140	Submit Draft BA-1 Soil Letter Rpt (COWR)			0	0				10NOV05	0	★ Submit Draft BA-1 Soil Letter Rpt (COWR)																																																																							
BA0150	Prepare Final BA-1 Soil Letter Rpt (COWR)			75	75			14NOV05	03MAR06	0	■ Prepare Final BA-1 Soil Letter Rpt (COWR)																																																																							
BA0160	Submit Final BA-1 Soil Letter Rpt (COWR)			0	0				03MAR06	0	★ Submit Final BA-1 Soil Letter Rpt (COWR)																																																																							

Camp Edwards Wide Area Source Assessment

CEWASA - Generic Activities

CEWASA: Work Plan

02770	Prepare Draft CEWASA Work Plan			344*	0*	01MAR04A	12JUL05	01MAR04A	12JUL05A	0																																																																																				
02805	Submit Draft Generic CEWASA Work Plan			0	0		12JUL05		12JUL05A	0																																																																																				
02806	Prepare Final Generic CEWASA Work Plan			100*	72*	13JUL05	27OCT05	13JUL05A	05DEC05	-25	■ Prepare Final Generic CEWASA Work Plan																																																																																			
02885	Submit Final Generic CEWASA Work Plan			0	0		27OCT05		05DEC05	-25	★ Submit Final Generic CEWASA Work Plan 25 day delay - extended EPA comment duration																																																																																			
02888	PLACEHOLDER: WASA: RRA			274	274	01SEP06*	28SEP07	01SEP06*	28SEP07	0	■ PLACEHOLDER: WASA: RRA																																																																																			
02887	PLACEHOLDER: WASA: RI			589	589	01SEP05*	31DEC07	01SEP05*	31DEC07	0	■ PLACEHOLDER: WASA: RI																																																																																			

milestone colors

- Milestone > 90 days Out
- Milestone < 90 days Out

Activity ID	Activity Description	Enforceable Milestone	Orig Dur	Rem Dur	Early Start RCS 52205	Early Finish RCS 52205	Anticipated Start	Anticipated Finish	Variance	Timeline												
										2005	2006			2007			2008			2009		
Small Arms Range																						
Small Arms Range: Remedial Investigation																						
01591	Prepare Draft SAR RI Workplan			88	0	04OCT04A	28FEB05A	04OCT04A	28FEB05A	0												
01592	Submit Draft SAR RI Workplan			0	0		28FEB05A		28FEB05A	0												
01594	Prepare Final SAR RI Workplan			75	60	01MAR05A	16AUG05	01MAR05A	16NOV05	-63	Prepare Final SAR RI Workplan awaiting agency comments											
01595	Submit Final SAR RI Workplan			0	0		16AUG05		16NOV05	-63	Submit Final SAR RI Workplan Submittal is 20 Days from MOR Approval											
01597	Implement SAR RI Field Program			39	39	03OCT05*	29NOV05	22NOV05*	19JAN06	-34	Implement SAR RI Field Program Note: Fieldwork scheduled after peak training season.											
01607	Validate Data SAR RI Field Program			57	57	03NOV05	27JAN06	23DEC05	17MAR06	-34	Validate Data SAR RI Field Program											
01598	Prepare Draft SAR RI Report			135	135	07DEC05	20JUN06	27JAN06	08AUG06	-34	Prepare Draft SAR RI Report											
01601	Submit Draft SAR RI Report	09MAY06		0	0		20JUN06		08AUG06	-34	Submit Draft SAR RI Report											
01602	Prepare Final SAR RI Report			75	75	21JUN06	05OCT06	09AUG06	27NOV06	-34	Prepare Final SAR RI Report											
01599	Submit Final SAR RI Report			0	0		05OCT06		27NOV06	-34	Submit Final SAR RI Report Submittal is 20 Days from MOR Approval											
01756	PLACEHOLDER: SAR: FS			223	223	21JUN06	08MAY07	09AUG06	25JUN07	-34	PLACEHOLDER: SAR: FS											
Small Arms Range: RRA																						
01800	Prepare Draft SAR RRA Work Plan			30	30	03JAN06*	14FEB06	03JAN06*	14FEB06	0	Prepare Draft SAR RRA Work Plan											
01802	Submit Draft SAR RRA Work Plan	14FEB06		0	0		14FEB06		14FEB06	0	Submit Draft SAR RRA Work Plan											
01804	Prepare Final SAR RRA Work Plan			75	75	15FEB06	01JUN06	15FEB06	01JUN06	0	Prepare Final SAR RRA Work Plan											
01806	Submit Final SAR RRA Work Plan			0	0		01JUN06		01JUN06	0	Submit Final SAR RRA Work Plan Submittal is 20 Days from MOR Approval											
01808	PLACEHOLDER: Implement SAR RRA Field Program			30	30	04MAY06	15JUN06	04MAY06	15JUN06	0	PLACEHOLDER: Implement SAR RRA Field Program											
01810	Lab Analysis Data Validation SAR RRA			50	50	24MAY06	03AUG06	24MAY06	03AUG06	0	Lab Analysis Data Validation SAR RRA											
01812	Prepare Draft SAR RRA Completion of Work Rt			45	45	04AUG06	06OCT06	04AUG06	06OCT06	0	Prepare Draft SAR RRA Completion of Work Rt FS will be added in the future, if the RRA does not reduce contaminants to below risk levels.											
01814	Submit Draft SAR RRA Completion of Work Rt	06OCT06		0	0		06OCT06		06OCT06	0	Submit Draft SAR RRA Completion of Work Rt											
01816	Prepare Final SAR RRA Completion of Work Rt			75	75	10OCT06	26JAN07	10OCT06	26JAN07	0	Prepare Final SAR RRA Completion of Work Rt											
01818	Submit Final SAR RRA Completion of Work Rt			0	0		26JAN07		26JAN07	0	Submit Final SAR RRA Completion of Work Rt Submittal is 20 Days from MOR Approval											
Training Area																						
Training Areas																						
Training Areas																						
00870	Prepare Draft Training Areas Data Summary Report			63	0	09NOV04A	14FEB05A	09NOV04A	14FEB05A	0												

Activity ID	Activity Description	Enforceable Milestone	Orig Dur	Rem Dur	Early Start RCS 52205	Early Finish RCS 52205	Anticipated Start	Anticipated Finish	Variance	2005												2006												2007												2008												2009												2010												
00880	Submit Draft Training Areas Data Summary Report			0	0		14FEB05A	14FEB05A	0																																																																									
00890	Prepare Final Training Areas Data Summary Report			75	60	15FEB05A	16AUG05	15FEB05A	16NOV05	-63																																																																								
00895	Submit Final Training Areas Data Summary Report			0	0		16AUG05		16NOV05	-63																																																																								

Prepare Final Training Areas Data Summary Report
 FS is not currently scheduled since soil contaminants are expected to be below risk based levels.

Submit Final Training Areas Data Summary Report
 Submittal is 20 Days from MOR Approval
 63 day delay - extended EPA comment duration

milestone colors

- Milestone > 90 days Out
- Milestone < 90 days Out
